



MANAGEMENT PLAN

SNOWY 2.0 MAIN WORKS – POLLUTION INCIDENT RESPONSE MANAGMENT PLAN

S2-FGJV-ENV-PLN-0091

APRIL 2024

ABSTRACT

The Plan is a requirement of the Main Works EPL and outlines the procedures in place to minimise the risk of a pollution incident occurring on the premises of the Main Works Project site including notification, action and communication procedures to manage pollution incidents.

Revision Record

Rev.	Date	Reason for Issue	Responsible	Accountable	Endorsed
D	03.04.2024	Revised based on findings of the annual review	J Okori	E Porter	M Franceschi





Document Verification

RACIE Record	
R esponsible:	Name: Jima Okori & Jemma Vivian Job Title: Environmental Coordinator Signed: Date: 04.06.2024
A ccountable:	Name: Ellen Porter Job Title: Environment Manager
	Signed: Date: 04.06.2024 See distribution list on Page 3.
C onsulted:	
I nformed:	See distribution list on Page 3.
E ndorsed:	Name: Massimo Franceschi Job Title: Project Director Signed: Date: 4/06/2024

RACIE Terms

R	Responsible
ĸ	The person who actually produces the document.
~	Accountable
Α	The person who has the answer for success or failure of the quality and timeliness of the document.
С	Consulted
C	Those who must be consulted before the document is published.
	Informed
•	Those who must be informed after the document is published.
E	Endorsed
	Those who must approve the document before publication.





Document Distribution Consulted Distribution List

Date	Format (1)	Addressee / Job Title	Company	Location (2)
Informed Di	stribution	list		

Informed Distribution List

Date	Format (1)	Addressee / Job Title	Company	Location (2)

NOTE:

```
(1) OHC - Original Hard Copy / EC-Electronic Copy / HC - Hard Copy / Aconex -Electronic Document Management System
```

Revision Tracking

Rev.	Date	Description of Revision
Α	19.08.2020	Rev A for SHL review
В	21.09.2020	Rev B incorporating SHL comments
С	31.05.2023	Revised based on findings of the annual review
D	02.04.2023	Revised based on findings of the annual review





CONTENTS

ABB	REVIATIONS AND DEFINITIONS	5
1.	INTRODUCTION	8
1.1.	Project Description	8
	1.1.1. Overview	8
	1.1.2. Main Works Construction Activities and Program	8
1.2.	Purpose	9
2.	ENVIRONMENTAL REQUIREMENTS	10
2.1.	Legislation	10
2.2.	Guidelines	10
3.	RESPONSIBILITIES	
4.	DESCRIPTION OF HAZARD AND LIKELIHOOD	12
5.	PRE-EMPTIVE ACTIONS TO BE TAKEN	13
5.1.	Inspections	13
5.2.	Monitoring Programs	14
6.	INVENTORY OF POLLUTANTS	17
7.	SAFETY EQUIPMENT	17
8.	NOTIFICATION	18
8.1.	What is a pollution incident	18
8.2.	Types of Incidents to be Notified	19
8.3.	Notification Process	19
8.4.	Information to be Reported	21
9.	COMMUNICATING WITH NEIGHBOURS AND LOCAL COMMUNITY	21
10.	MINIMISING HARM TO PERSONS ON THE PREMISES	22
11.	ACTIONS TO BE TAKEN DURING OR IMMEDIATELY AFTER A POLLUTION INCIDENT	22
12.	TRAINING	25
13.	AVAILABILITY	25
14.	TESTING AND REVIEW	25
15.	MAPS	28
APPE	ENDIX A – COMPLIANCE MATRIX	29
	ENDIX B – ENVIRONMENTAL ASPECTS AND IMPACTS REGISTER	
APPE	ENDIX C – EXAMPLE INVENTORY OF POLLUTANTS	56
APPE	ENDIX E – EPL PREMISE AREA MAPS	58

TABLES

Table 3-1: Response personnel contact details	11
Table 4-1: Risk Matrix	12
Table 4-2: Likelihood table	12
Table 5-1: Inspection schedule summary	14
Table 5-2: Monitoring programmes summary	15
Table 8-1: Pollution Incident Types	19
Table 8-2: PIRMP Agency Notification Contact Details	20
Table 8-3: Other Agencies	21
Table 14-1: Testing Elements Tracking	27





ABBREVIATIONS AND DEFINITIONS

Acronym	Definition
AfL	Agreement for Lease with NPWS
ANZECC	Australian and New Zealand Environment and Conservation Council
APZ	Asset Protection Zone
AS/NZ	Australian Standard/ New Zealand Standard
BC Act	Biodiversity Conservation Act 2016
BCD	Biodiversity and Conservation Division (part of Department of Planning, Industry and Environment)
BMP	Biodiversity Management Plan
BMS	Future Generation Business Management System
ВоМ	Bureau of Meteorology
CNMP	Construction Noise Management Plan – Rock Forest
Contractor	WeBuild (formerly Salini Impregilo), Clough and Lane have formed the Future Generation Joint Venture (Future Generation). Future Generation is the contractor who will be carrying out the Snowy 2.0 Main Works on behalf of Snowy Hydro Limited. References to the Contractor in this Environmental Management Strategy refers to Future Generation and includes all its sub- contractors.
Construction envelope	The envelope within which the disturbance area of the development may be located.
CSSI	Critical State significant infrastructure
Cth	Commonwealth
DAWE	The Commonwealth Department of Agriculture, Water and the Environment which is responsible for administering the <i>Environment Protection and Biodiversity Conservation Act</i> 1999.
Development	The development of the Exploratory Works and Main Works as modified by the conditions of this approval
Disturbance area	The area within the construction envelope where the development may be carried out.
DPIE or Department	NSW Department of Planning, Industry and Environment
DPI Fisheries	Department of Primary Industries – Fisheries
EIS	Snowy 2.0 Main Works - Environmental Impact Statement
EMS	Environmental Management Strategy
Environmental aspect	Defined by AS/NZS ISO 14001:2004 as an element of an organisation's activities, products or services that can interact with the environment
Environmental impact	Defined by AS/NZS ISO 14001:2004 as any change to the environment, whether adverse or beneficial, wholly or partially resulting from an organisation's environmental aspects
Environmental objective	Defined by AS/NZS ISO 14001:2004 as an overall environmental goal, consistent with the environmental policy, that an organisation sets itself to achieve
Environmental policy	Statement by an organisation of its intention and principles for environmental performance
Environmental target	Defined by AS/NZS ISO 14001:2004 as a detailed performance requirement, applicable to the organisation or parts thereof, that arises from the environmental objectives and that needs to be set and met in order to achieve those objectives
EP&A Act	Environmental Planning and Assessment Act 1979
EPBC Act	Environment Protection and Biodiversity Conservation Act 1999
EPA	NSW Environment Protection Authority





Acronym	Definition
EPL	Environment Protection Licence
ERMP	Emergency Response Management Plan
ESCP	Erosion and Sediment Control Plan
Exploratory Works	The development of an exploratory tunnel and associated infrastructure described in the Environmental Impact Statement for the Snowy 2.0 Exploratory Works (CSSI 9208) dated July 2018, and modified by the:
	Submissions Report dated October 2018 and additional information provide to the Department on 17 October 2018, 19 November 2018 and 23 January 2019;
	 Modification Report dated 6 June 2019, associated Submissions Report dated 2 September 2019 and amendment letter dated 4 October 2019; and
	Modification Report dated 17 October 2019 and associated Submissions Report dated 10 January 2020.
Exploratory Works EIS	Environmental Impact Statement Exploratory Works for Snowy 2.0
FAB	Fresh Air Base
FRNSW	NSW Fire and Rescue
Future Generation	Future Generation Joint Venture
GWMP	Groundwater Management Plan
HMP	Heritage Management Plan
HV	Heavy Vehicle
Incident	An occurrence or set of circumstances that causes or threatens to cause material harm and which may or may not be or cause a non-compliance (<i>Infrastructure Approval – CSSI 9687</i>).
ISO	International Standards Organisation
KNP	Kosciusko National Park
Main Works	The development of an underground power station and associated infrastructure described in the Environmental Impact Statement for the Snowy 2.0 Main Works (CSSI 9687) dated September 2019, and modified by the:
	 Preferred Infrastructure Report and Response to Submissions – Snowy 2.0 Main Works, dated February 2020; and
	Additional information provided to the Department by EMM on 24 March 2020 and 7 April 2020.
Main Works EIS	Snowy 2.0 Main Works - Environmental Impact Statement
MNES	Matters of national environmental significance under the EPBC Act 1999
NATA	National Association of Testing Authorities
NEM	National Electricity Market
NPW Act	National Parks and Wildlife Act 1974
NPWS	National Parks and Wildlife Services
NSW	New South Wales
NSW DPI	The NSW Department of Primary Industries within Regional NSW
OSOM	Oversize Overmass
Occupier, the	the person who has the management or control of the premises (Future Generation)
PIRMP	Pollution Incident Response Management Plan (this plan)





Acronym	Definition
POEO Act	Protection of the Environment Operations Act 1997
POEO(G) Reg	Protection of the Environment Operations (General) Regulation 2009
POEO Reg Amendment	Protection of the Environment Operation Amendment Regulation 2012
РоМ	Plan of Management
Project, the	Snowy 2.0 Main Works
Project area	The broader region within which Snowy 2.0 will be built and operated, and the extent within which direct impacts from Snowy 2.0 Main Works are anticipated.
RTS or Submissions Report	Snowy 2.0 Main Works – Response to Submissions
SAP	Sensitive Area Plans
Snowy 2.0	A pumped hydro-electric expansion of the Snowy Scheme that will link the two existing reservoirs of Tantangara and Talbingo through underground tunnels, and include a new underground power station with pumping capabilities
Snowy Hydro	Snowy Hydro Limited
SES	State Emergency Services
SMP	Spoil Management Plan
SWMP	Surface Water Management Plan
TARP	Trigger Action Response Plan
ТВМ	Tunnel Boring Machine
TfNSW	Transport for NSW
Waste MP	Waste Management Plan
WMP	Water Management Plan





1. INTRODUCTION

1.1. **Project Description**

1.1.1. Overview

Snowy Hydro Limited (Snowy Hydro) is constructing a pumped hydro-electric expansion of the Snowy Mountains Hydro-electric Scheme (Snowy Scheme), called Snowy 2.0. Snowy 2.0 is being built in two stages: Exploratory Works (which is completed) and Snowy 2.0 Main Works (which commenced in October 2020).

Snowy 2.0 is a pumped hydro-electric project that will link the existing Tantangara and Talbingo reservoirs through a series of new underground tunnels and a hydro-electric power station. Most of the project's facilities will be built underground, with approximately 27 kilometres of concrete-lined tunnels constructed to link the two reservoirs and a further 20 kilometres of tunnels required to support the facility. Intake and outlet structures will be built at both Tantangara and Talbingo Reservoirs.

Snowy 2.0 will increase the generation capacity of the Snowy Scheme by an additional 2,000 MW, and at full capacity will provide approximately 350,000 MWh of large-scale energy storage to the National Electricity Market (NEM). This will be enough to ensure the stability and reliability of the NEM, even during prolonged periods of adverse weather conditions.

WeBuild (formerly Salini Impregilo), Clough and Lane have formed the Future Generation Joint Venture (Future Generation) and have been engaged to deliver Snowy 2.0 Main Works. This Pollution Incident Response Management Plan (PIRMP, and this plan) has been prepared for Snowy 2.0 Main Works.

1.1.2. Main Works Construction Activities and Program

The Snowy 2.0 project includes, but is not limited to, construction of the following:

- pre-construction preparatory activities including dilapidation studies, survey, investigations, access etc;
- Exploratory Works including:
 - an exploratory tunnel to the site of the underground power station;
 - horizontal and test drilling;
 - a portal construction pad;
 - an accommodation camp;
 - barge access infrastructure;
- an underground pumped hydro-electric power station complex;
- water intake structures at Tantangara and Talbingo reservoirs;
- power waterway tunnels, chambers and shafts;
- access tunnels;
- new and upgraded roads to allow ongoing access and maintenance;
- power, water and communication infrastructure, including:
 - a cable yard to facilitate connection between the NEM electricity transmission network and Snowy 2.0;





- permanent auxiliary power connection;
- permanent communication cables;
- permanent water supply to the underground power station; and
- post-construction revegetation and rehabilitation.

The Snowy 2.0 construction program is summarised in Figure 1-1.

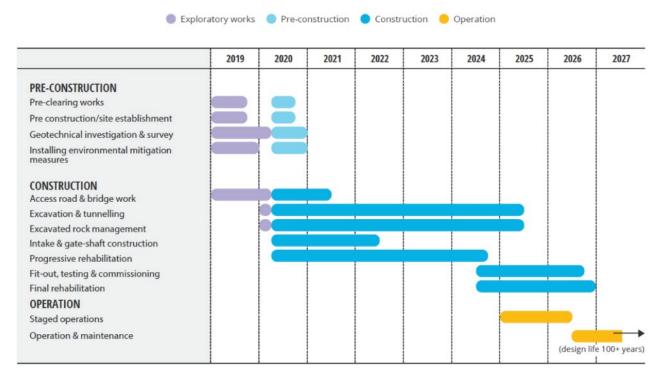


Figure 1-1: Indicative Timing of Snowy 2.0 Exploratory Works and Main Works

1.2. Purpose

The works required to be undertaken for Snowy 2.0 Main Works include scheduled activities, which require licensing under the *Protection of the Environment Operations Act 1997* (POEO Act).

Environment Protection Licence (EPL) 21266 has been issued for the project for the scheduled activity of extractive activities for the Exploratory Works and the construction of the Main Works phases. The premises boundary for the Exploratory Works EPL has been expanded to encompass both Exploratory Works and Main Works. The e governing scheduled activity for Main Works was revised to electricity generation.

All scheduled activities licensed by the Environment Protection Licence (EPL) will be subject to this Pollution Incident Response Management Plan (PIRMP or plan), including the remainder of Exploratory Works and the duration of Main Works. Revision of this PIRMP will be undertaken on annual basis.

This plan has been prepared in accordance with the legislative requirements for a PIRMP prescribed in the POEO Act, the *Protection of the Environment Operations (General) Regulation 2009* (POEO(G) Reg), the *Protection of the Environment Operation Amendment Regulation 2012* (POEO Reg Amendment) and the conditions in the EPL (21266).





There is no external agency or regulator approval required for the PIRMP.

This plan outlines the procedures in place to minimise the risk of a pollution incident occurring on the premises including notification, action and communication procedures to manage pollution incidents.

Construction personnel will be required to undertake works in accordance with this plan.

The objectives of this plan are to:

- ensure comprehensive and timely communication of a pollution incident;
- minimise and control the risk of a pollution incident through identification of risks and the development of planned actions to minimise and manage those risks;
- ensure responsibilities are assigned and training in pollution incident response is undertaken; and
- ensure the plan is implemented, tested and reviewed.

2. ENVIRONMENTAL REQUIREMENTS

2.1. Legislation

Legislation relevant to air quality management includes:

- Protection of the Environment Operations Act 1997 (POEO Act);
- Protection of the Environment Operations (General) Regulation 2009 (POEO(G) Reg); and
- Protection of the Environment Operations (General) Amendment (Pollution Incident Response Management Plans) Regulation 2012 (POEO(G) Reg Amendment).

Relevant provisions of the above legislation are explained in the register of legal and other requirements included in Appendix A2 of the EMS. Compliance of this document with relevant sections of the POEO Act and project EPL are demonstrated in Appendix A.

2.2. Guidelines

The plan has been developed in accordance with the NSW EPA *Preparation of Pollution Incident Response Management Plans* (2012).





3. **RESPONSIBILITIES**

In the event of an incident, the personnel who are immediately involved on-site or witness the event are responsible to act appropriately by way of immediately notifying the event or the observation of a potential event to the Site Supervisor and a member of the Health, Safety and Environment (HSE) Team.

The personnel immediately involved are also required to act appropriately by, only if safe to do so, attend the event to try and cease the event or minimise its impact.

The Site Supervisor and / or HSE Team must report the event or potential event to the relevant response personnel including the General Superintendent, Construction Manager and Environment Manager. These response personnel are responsible for:

- managing the response to a pollution incident, and
- activating the PIRMP including notifying external relevant authorities.

Table 3-1 details the names, position titles and 24-hour contact details of the key response personnel.

Table 3-1: Response personnel contact details

Position	24-Hour Contact
Environment Manager – Ellen Porter	0466 876 865
Construction Manager Lobs Hole – William Binsted	0458 237 447
Construction Manager Marica – Pierangelo Sorbelli	0429 539 652
Construction Manager Tantangara – Matteo Passarani	0481 917 629
General Superintendent Lobs Hole – Anthony Wynd	0437 151 773
General Superintendent Marica – Brendan Hall	0401 158 666
General Superintendent Tantangara – Matt Gardener	0406 842 268
Health Safety, Security & Environment Manager – Steve Thorne	0499 835 909
Deputy Health Safety, Security & Environment Manager – Peter Cook	0429 087 637
Security Manager – Graham Bennett	0498 345 199
Security Coordinator – Brendan Barnes	0475 635 654

Note: Contact details will be updated on a regular basis on the site environmental incident response contact sheet.





4. DESCRIPTION OF HAZARD AND LIKELIHOOD

Hazards to human health or the environment, the likelihood of the hazards occurring and the mechanisms to manage that risk were assessed as part of the Main Works EMS environmental (aspects and impacts) risk assessment. This risk assessment details the environmental aspects identified for the project, the initial risk category prior to appropriate management strategies, and reference to the appropriate document which detailing proposed mitigation strategies. A copy of the (aspects and impacts) risk register is presented in Appendix B.

The ongoing determination of environmental aspects and impacts will be achieved through the risk management processes outlined in Section 4.3 of the EMS, which results in the maintenance of a list of environmental risks (aspects and impacts), corresponding risk mitigation strategy and risk ranking for each risk. Each environmental risk is categorised, based on the following:

- the environmental aspect;
- type of potential impact (or consequence); and
- likelihood of occurrence.

A risk matrix for the initial environmental risk assessment is provided in Table 4-1.

Table 4-1: Risk Matrix

	Likelihood					
Consequence	1 – Rare	2 – Unlikely	3 – Possible	4 – Likely	5 – Almost Certain	
5 – Severe	5 – Medium	10 – High	15 – High	20 – Extreme	25 – Extreme	
4 – Major	4 – Medium	8 – Medium	12 – High	16 – High	20 – Extreme	
3 – Moderate	3 – Low	6 – Medium	9 – Medium	12 – High	15 – High	
2 – Minor	2 – Low	4 – Low	6 – Medium	8 – Medium	10 – Medium	
1 – Insignificant	1 – Low	2 – Low	3 – Low	4 – Low	5 – Medium	

Descriptions provided in Table 4-2 were used to determine the likelihood and consequence of an event.

Table 4-2: Likelihood table

Likelihood	Description
Almost Certain	Historically, the event has been known to occur very frequently, based on comparisons with similar projects conducted under similar conditions. Based on current project circumstances, the event is expected to occur over the course of this project.
Likely	Historically, the event has been known to occur frequently, based on comparisons with similar projects conducted under similar conditions. Based upon current project circumstances, were it to occur over the course of this project, the event would be considered unremarkable.
Possible	Historically, the event has been known to occur, based on comparisons with similar projects conducted under similar conditions. Based upon current project circumstances, it is plausible for this event to occur over the course of this project.
Unlikely	Historically, the event has been known to occur infrequently, based on comparisons with similar projects conducted under similar conditions. Based upon current project circumstances, were it to occur over the course of this project, the event would be considered remarkable.





Rare	Historically, the event has occurred very infrequently, based on comparisons with similar projects conducted under similar conditions. Based upon current project circumstances, were the event to occur over the course of the project, the event would be considered exceptional.
Likelihood	Description
Negligible	Promptly reversible/trivial impact on air, water, soil, flora, fauna, habitat or heritage.
Minor	Short term (1-3 year) impact on population of native flora or fauna. Short term impacts on soil, air, water quality or habitat. Impact mostly confined to work area but potential short-term off-site impacts. Adverse impact to significant (e.g. category A and B) heritage items. Visual, noise or airborne dust impacts with potential for credible stakeholder/public complaint
Moderate	Medium term (3-10 year) impact on population of native flora or fauna. Medium term impacts on soil, air, water quality or habitat. Potential for medium term off- site impacts. Loss of a significant heritage items. Visual, noise or airborne dust impacts with potential for regular response.
Major	Long term (>10 years) impact on population of significant (e.g. threatened) flora or fauna. Long term impacts on soil, air, water quality. Potential for long term offsite impacts. Loss of numerous significant heritage items.
Severe	Permanent impact on the populations of the significant (e.g. threatened) flora or fauna. Permanent unconfined impact on previously undisturbed ecosystem.

5. PRE-EMPTIVE ACTIONS TO BE TAKEN

Future Generation will undertake pre-emptive measures including training, inspections and monitoring outlined in the EMS and supporting sub-plans, summarised below, to minimise or prevent any risk of harm to human health or the environment arising out of the scheduled activities conducted by Future Generation.

5.1. Inspections

Control measures will be inspected on a weekly basis by Future Generation's HSE Team. The purpose of the weekly checklist is to:

- provide a surveillance tool to ensure that safeguards are being implemented and housekeeping is maintained;
- identify where problems might be occurring;
- identify where sound environmental practices are not being implemented; and
- facilitate the identification and early resolution of problems.

Improvements and required actions will be analysed and prioritised at the completion of the inspection and timeframes for implementation of corrective actions agreed. Any non-conformances identified through the checklist process will be highlighted and an environmental inspection report (minor issues) or an environmental incident report completed.

The issue will remain 'open' until:

- the issue has been resolved;
- a new or revised procedure has been established and implemented; or
- training has been provided to relevant personnel/ sub-contractors.

The findings of inspections will be discussed at toolbox meetings and issues raised will be considered by the Future Generation project management team for review or improvement of the environment procedures.

An inspection schedule is provided in Table 5-1.





Table 5-1: Inspection schedule summary

Activity	Frequency	Responsibility	Record
Environmental site inspection	Weekly	Future Generation Environmental Manager or nominated representative. Snowy Hydro to be invited at the discretion of Future Generation.	Site inspection checklist.

5.2. Monitoring Programs

Monitoring will be undertaken for environmental aspects of the project to confirm the adequacy of implementation of the management measures and will highlight any non-conformances or potential non-conformances during construction of the project. Specific monitoring programs have been developed for high-risk aspects of the project and these are included within the relevant management plans.

The monitoring programs have been developed to address the requirements of the conditions of Approval and project EPL. In general, these require that:

- baseline data available, additional data to be obtained and timing;
- the parameters to be monitored and the location and frequency;
- the reporting of monitoring and analysis results against relevant criteria;
- methods that will be used to analyse the monitoring data; and
- procedures to identify and implement additional mitigation measures where results of monitoring are unsatisfactory; and
- any consultation to be undertaken in relation to the monitoring programs.

The timing, frequency, methodology, locations and responsibilities for the proposed environmental monitoring programs are specified in the respective management plans and summarised in Table 5-2. The monitoring programs range from those involving formal sample collection, analysis and measurement, to those involving a more qualitative assessment. This table is subject to update based on developments of the EMS and associated sub-plans relevant to each monitoring item.





Table 5-2: Monitoring programmes summary

Activity	Management Plan	Frequency	Responsibility	Record	Timing
EPL required					
Receiving surface water monitoring Comprehensive Sampling (in accordance with EPL 21266)	Surface Water Management Plan (SWMP) Spoil Management Plan (SMP)	In accordance with the approved SWMP	Future Generation HSE Team	Field sampling (survey 123) records and laboratory tests reports; Monthly water reports	In-situ – Weekly Comprehensive – Monthly
					TARP – Outside of Expected range
Waste Management (Construction Waste, Contaminated Soils, Oily Waste & General Waste)	Waste management Plan (WMP)	In accordance with the approved WMP	Future Generation HSE Team	Waste Dockets, Waste Management Record	Daily, Weekly & On- call basis
Air quality & Dust Monitoring	Air Quality Management Plan	In accordance with the approved AQMP	Future Generation Drill & Blast / TBM Teams HSE Team	D&B - Air and Dust & Lux Monitoring	Continuous inside the tunnels and at the accommodation camps
Groundwater quality monitoring	Groundwater Management Plan (GMP) Spoil Management Plan (SMP)	In accordance with the approved GMP	Future Generation HSE Team	Field sampling and testing records and NATA tests reports; Quarterly groundwater reports Field sampling and testing records and NATA tests reports;	Quarterly In-situ – Weekly Comprehensive – Monthly
					TARP – Outside of Expected range
Noise	Construction Noise Management Plan	In accordance with approved CNMP	Snowy Hydro Environment Team	Noise Monitoring records	Monthly
Extreme weather monitoring and TARP	Emergency Response Management Plan Surface Water Management Plan (SWMP) Erosion and Sediment Control Plan	In accordance with the approved SWMP	Future Generation HSE Team/ Site Supervisors	ESC Checklists Pre-rainfall Inspection records Post-rainfall Inspection records Field sampling (survey 123) records and laboratory tests reports	As per rain events. Weekly during normal construction hours; Prior to forecast rainfall (>50% chance of 10mm or more in 24 hours),





Activity	Management Plan	Frequency	Responsibility	Record	Timing
					Daily during rain events (if safe to do so).
Spoil Monitoring (Excavated rocks)	Spoil Management Plan	In accordance with the	Future Generation	Inspection report	Lobs Hole:
		approved SMP	HSE Team/ Site Supervisors	Laboratory test report	TBM – 1 sample every 5 rings or 10m
					D&B – 1 sample every 8m
					Marica:
					2 samples every 1m depth.
					Tantagara:
					1 sample every 1000m ³
Spoil Emplacement (PSE)	Spoil Management Plan	In accordance with the	Future Generation	Field sampling and testing	Quarterly
		Surface and Groundwater	HSE Team/ Site	records and NATA tests reports;	In-situ – Weekly
	Surface Water Management	Management Plan	Supervisors / Site Engineers	Quarterly groundwater reports	
	Plan (SWMP)				Comprehensive – Monthly
	Groundwater Management Plan				
	(GMP)				TARP – Outside of Expected range





6. INVENTORY OF POLLUTANTS

An inventory of potential pollutants kept on the premises or used in carrying out activities at the premises is presented in Appendix C. The pollutant inventory will be maintained by relevant teams assisted by the HSE and copies provided to the Medical Teams. The inventory includes the pollutant type, maximum quantity that is likely to be held and the details of the pollutant storage locations.

7. SAFETY EQUIPMENT

Equipment will be available and implemented proactively and reactively to an incident to minimise harm to human health and the environment. Storages of physical environmental equipment to minimise the harm of an event are shown on the Sensitive Area Plans (SAPs) which are updated over time to reflect current works being undertaken.

Environmental equipment includes:

- maintaining areas of avoidance (No-Go Zones) for sensitive environments;
- designated storage areas with bunding for hazardous chemicals (with Safety Data Sheets held online and on site for ready access by project personnel); and
- spill kits.

Other physical environmental controls include progressive erosion and sediment controls, and permanent drainage control infrastructure and. Note that these controls are shown on progressive Erosion and Sediment Control Plans (ESCP), separate to this PIRMP.

Physical human health equipment available to minimise the harm of an event to both personnel and the environmental, will include:

- Emergency Response Bases: Located at Future Generation main site office, Emergency Response Bases (ERB) will be the assembly and staging areas for the emergency team and the principal emergency response equipment storage areas. Satellite emergency response facilities (ERF) will also be established adjacent to the main work sites at the MAT portal access to support the underground works, including the cavern and at Tantangara and Marica. The Lobs Hole ERB will support the Talbingo works;
- Emergency response equipment associated with a helicopter emergency will be provided adjacent to helicopter landing sites (HLS) located at Lobs Hole, Tantangara and Marica Trail camps;
- Work Boat: The project will be equipped with a work boat for use in emergencies and will always be on the water when marine activities are being undertaken.
- Firefighting equipment (surface):
 - Work sites and camp areas will include:
 - Exploratory Camp: firefighting water line with electric (diesel backup) pumps connected to two (2) dual purpose 500kL tanks to service hydrants and hose reels;
 - Main Yard: firefighting water line with electric (diesel backup) pumps connected to two
 (2) dual purpose 500kL tanks to service hydrants and hose reels;
 - Marica Camp: firefighting water line with electric (diesel backup) pumps connected to two
 (2) dual purpose 110kL tanks to service hydrants and hose reels;
 - Tantangara Camp: firefighting water line with electric (diesel backup) pumps connected to a dual purpose 500kL tank to service hydrants and hose reels;





- All accommodation, offices and buildings associated with the construction facilities will be fitted with smoke alarms and fire extinguishers and there will be a minimum 20,000L dedicated fire water supply (rainwater roof collected, topped up by water cart) fitted with Storz bushfire couplings at the camps to enhance the early detection of fires and local firefighting capability;
- All construction facilities such as the fabrication warehouse and slurry treatment plant will be assessed and fitted with specific firefighting equipment with a local water supply (e.g. tank) provided;
- Category 9 fire unit vehicles will be available to respond from each of the emergency control centres and will carry pumps, firehoses, fire suppression chemicals and 600L of water. Water supply for surface fires will be provided using project water trucks. All mobile plant, HV and LV on the project will be fitted with portable fire extinguishers to enable prompt initial response to vehicle fires;
- Firefighting equipment (underground): During the construction of the underground tunnels, the tunnels will be supplied with:
 - water for firefighting via a pipeline from the surface fitted with 40mm firehose connectors that are 50m apart;
 - a multi-service vehicle (MSV) fitted with a 25m firehose will be deployed with an Emergency Response Team (ERT) to fight fires within the tunnel;
 - the tunnel boring machine (TBM) will be fitted with an integrated refuge chamber for use by the operational team in the case of fire or another emergency. The refuge chamber has a capacity for 24 workers for a period of 24 hours when disconnected from the tunnel air line.
 - 6kg dry chemical portable fire extinguishers will be positioned on the TBM at identified firerisk areas, e.g. the power switch boards;
 - the TBM will be contain sprinkles all along gantries and a water curtain at the final gantry to confine smoke and dust;
 - the TBM will also contain, automatic fire and gas detectors and an automatic fire suppression system at emergency generators, hydraulic tanks, and cabinets.
- Emergency response personnel: Future Generation have an experienced team responsible for managing and coordinating responses to emergencies.

8. NOTIFICATION

8.1. What is a pollution incident

A pollution incident is defined in Section 147 of the POEO Act as:

- a) harm to the environment is material if:
 - (i) it involves actual or potential harm to the health or safety of human beings or to ecosystems that is not trivial, or
 - (ii) it results in actual or potential loss or property damage of an amount, or amounts in aggregate, exceeding \$10,000 (or such other amount as is prescribed by the regulations), and
- b) loss includes the reasonable costs and expenses that would be incurred in taking all reasonable and practicable measures to prevent, mitigate or make good harm to the environment.





For the purposes of section 147, it does not matter that harm to the environment is caused only in the premises where the pollution incident occurs.

8.2. Types of Incidents to be Notified.

Table 8-1 details examples of incidents required to be reported. The emission of odour from the premises is not required to be reported under the POEO Act Part 5.7 clause 148(7).

Incident Type	Description
Works occurring beyond the EPL premised boundary	Where scheduled activities occur beyond the EPL premised boundary without prior approval from the EPA and the event meets the definition of pollution incident.
Air quality	Where the emission of dust from the EPL premised boundary occurs as a result of activities being carried out in a manner that does not minimise or prevent the emission and meets the definition of pollution incident.
Chemical spills	Where a chemical spill occurs either within or beyond the premised boundary where that cannot easily be remediated and the event meets the definition of pollution incident.
Waste disposal	Where waste is known to have been transported and/or transported to a place that cannot lawfully accept the waste and the event meets the definition of pollution incident.
Water discharge from premises	Any results of in situ monitoring within the licensed premises listed in the EPL that exceed the maximum values, or are outside the range of, a relevant 'predicted discharge water quality characteristic' specified in Section 2 of the Main Works Surface Water Monitoring Program (Appendix B of the Main Works Surface Water Management Plan) and the event meets the definition of pollution incident.
	Discharge of treated process and/or sewage wastewater that does not meet the treatment criteria within the Section 2 of the Main Works Surface Water Monitoring Program (Appendix B of the Main Works Surface Water Management Plan) and the event meets the definition of pollution incident.
	Discharge of treated surface water that does not meet the discharge criteria within the Section 2 of the Main Works Surface Water Monitoring Program (Appendix B of the Main Works Surface Water Management Plan) where an overflow rain event has not occurred and the event meets the definition of pollution incident.
Surface and ground water monitoring	Any results of in situ monitoring that exceed the maximum value, or are outside the range of, a relevant 'receiving water quality objective' specified in Section 2 of the Main Works Surface Water Monitoring Program (Appendix B of the Main Works Surface Water Management Plan), Groundwater Management Plan (S2-FGJV-ENV-PLN-0026-6 Table 6-2 Groundwater quality trigger value)and the event meets the definition of pollution incident.
	[Any other as specified in revised EPL]

 Table 8-1: Pollution Incident Types

Note: Reference to the project management plans and project EPL are subject to change.

8.3. Notification Process

Future Generation and Snowy Hydro Limited will jointly notify the EPA of pollution incidents within the EPL Licence premises via the EPA Environment Line (telephone 131 555) immediately after becoming aware of the incident, in accordance with Part 5.7 of the POEO Act. If Snowy Hydro personnel cannot be contacted, Future Generation will carry out the notification to EPA independently.

Table 8-2 details the relevant authorities who will be notified verbally in the event of a potential or actual pollution incident in compliance with POEO Act Part 5.7A clause 153C and any persons identified by Part 5.7. Table 8-3 identifies other agency contacts that Future Generation may notify in the event of a pollution incident, where it is appropriate and when it is practical to do so.





Co-ordination of any action taken in minimising the pollution caused by the incident will be undertaken between Future Generation and relevant authorities where appropriate, upon notification.

Either Future Generation (as the Employee under the legislation) or Snowy Hydro Limited (as the Employer, licensee and occupier under the legislation) will undertake notification of the relevant authorities. The Employee's (Future Generation) notification responsibilities can extend as an agent to the responsibilities of the Employer and/or Occupier under POEO Act Part 5.7 clause 148(6).

The Future Generation Environment Manager, HSE Manager, Project Director or an approved delegate are responsible for contacting the relevant authorities. Notification will occur as soon as feasibly possible immediately after an incident has occurred and the approved persons become aware of the incident. Notification will not occur if the person notifying of the incident is aware that the incident has already been reported to the relevant authorities.

Under Part 5.7 of the POEO Act Section 151 (2), any pollution caused during the clean-up or subsequent actions required to rectify an incident is not required to be notified.

Future Generation will comply with a direction from the EPA, in any form, to notify other persons of the pollution incident. Future Generation will undertake notification in writing within seven days of the date on which the incident occurred and submit to the EPA in response to the verbal notification of the incident. Future Generation will provide a report to the EPA in accordance with the EPL where required.

Organisation / Agency	Contact Details
Owners or occupiers of premises in the vicinity of t	he project
Snowy Hydro Limited ¹	Enviro Assurance Officers
National Parks and Wildlife Services ²	1800 629 104 (24/7)
	(02) 6450 5550 (Duty Officer)
	(Major projects portal also for incidents which require reporting under the Infrastructure Approval).
Local authority(s)	
Emergency Services:	000 (24/7)
Fire and Rescue NSW	
NSW Police	
NSW Ambulance	
Snowy Monaro Regional Council (Cooma)	1300 345 345 (24/7)
Snowy Valleys Council (Tumut)	1300 275 782 (24/7)
Appropriate regulatory authority(s)	
Environment Protection Authority (NSW Pollution Hotline)	Phone 131 555 (24/7)
NSW Ministry of Health, Goulburn Public Health Unit	(02) 4824 1837
	(02) 6080 8900 (after hours)
NSW Ministry of Health, Albury Public Health Unit	(02) 6080 8900 (24/7)
SafeWork NSW	13 10 50 (24/7)
Fire and Rescue NSW	(02) 6947 1202 (Tumut)
	(02) 6452 2037 (Cooma) (if 000 not already called)
Department of Planning, Industry and Environment ³	Major projects portal.

 Table 8-2: PIRMP Agency Notification Contact Details





Department of Planning, Industry and Environment Fisheries – Fishers' Watch Phoneline	00 043 536

- Whilst not listed as being notifiable under the POEO Act SHL hold EPL 21266 and, as an employer, also bear responsibility for 1. notifications under the Act.
- 2. Whilst not listed as being notifiable under the POEO Act NPWS are responsible for activities within Kosciuszko National Park.
- 3. Whilst not listed as being notifiable under the POEO Act, CSSI 9687 Sch 4 Cond 6 requires notification to the Department and NPWS via the Major Projects Portal immediately after it becomes aware of an incident as defined within the Infrastructure Approval. The notification will occur in accordance with section 7 of the EMS.

Table 8-3: Other Agencies

Organisation / Agency	Contact Details
State Emergency Service (SES)	13 25 00 (Cooma)
NSW Rural Fire Service	(02) 6981 4229 (Tumut)

8.4. Information to be Reported

All relevant, known information regarding the incident will be communicated at the time of notification. This includes:

- the time the incident occurred:
- the date that the incident occurred; •
- the nature of the incident:
- the duration the incident occurred;
- the location of the incident; •
- the location of the place where pollution is occurring or is likely to occur: •
- the estimated quantity or volume and the concentration of any pollutants involved, if known; •
- the circumstances in which the incident occurred including the cause, if known; and •
- the action(s) taken or proposed to be taken to deal with the incident and any resulting pollution . or threatened pollution, if known.

A report, in compliance with the EPL, will be provided to the NSW EPA within the required time frames stipulated in the Condition.

COMMUNICATING WITH NEIGHBOURS AND LOCAL COMMUNITY 9.

The project is in a remote location and the identified hazards and potential pollution incidents (in Appendix B) are not generally expected to impact any surrounding neighbours or local communities. Minor disruptions to the use of Tantangara and Talbingo Reservoirs will be managed through clear and regular community updates about project progress and impacts and targeted communications to park users to advise of reservoir access changes and alternatives. Potential noise impacts at the Rock Forest logistics yard will be managed in accordance with the Construction Noise Management Plan – Rock Forest and will include consultation with affected landholders.

Should incident communications be required, early warnings for affected or potentially affected community members for any pollution incident will be communicated to those members via phone calls and / or a door knock process.





For air pollution incidents that may affect community members, those community members may be asked to either close their doors and windows and stay indoors until further notice or vacate the premises. For water pollution incidents that may affect community members, those community members may be asked to avoid use of the water until further notice.

Future Generation may provide updates to the external community in consultation with SHL if required. Updated may be via letterbox drop, notices in local papers and/or via door knocks as required.

All other communications with interested parties and individuals within the neighbouring communities of the project, other than the relevant authorities detailed in Section 8, will be managed in accordance with the Community and Stakeholder Engagement Plan (CSEP) and will be coordinated with Snowy Hydro.

10. MINIMISING HARM TO PERSONS ON THE PREMISES

A pollution incident will trigger the enaction of this PIRMP and the processes it contains. The emergency response process includes:

- raising the alarm
- seeking assistance
- responding and controlling the incident.

Measures to minimise harm to persons on the premises include initiation and use of the following:

- Emergency Response Team
- Site medical centre and staffing
- Medical response
- Work boat
- Firefighting equipment underground and surface
- Refuge chambers
- Refuge chamber and Fresh Air Bases (FAB) equipment
- Direction to refuge chambers, FAB and lighting
- Emergency escape and breathing devices
- Grab bags
- Self-descent devices
- Lifebuoys

- Line throwing devices
- Safety showers and eye wash stations
- Helicopter crash rescue equipment
- Spill kits
- Gas detectors
- TBM firefighting system
- Extreme weather monitoring
- Helicopter search and rescue
- Incident control centre
- Emergency alarm systems underground
- Escape routes and exits
- Muster arrangements
- Site specific evacuation plans.

11. ACTIONS TO BE TAKEN DURING OR IMMEDIATELY AFTER A POLLUTION INCIDENT

In the event of an incident, Future Generation will immediately implement this PIRMP.

If a pollution incident occurs in the course of an activity at the premises so that actual or potential material harm to the environment is caused, Future Generation personnel will immediately





implement the Incident Response Process as shown in Figure 11-1. This process will be followed regardless if the event remains within or exists beyond the EPL premise boundary for Future Generation.

The emergency response process will implement corrective measures. Following an incident Future Generation will:

- undertake an investigation to attempt to determine the cause of the event and where appropriate:
 - establish and complete actions to rectify the identified catalyst(s) that contributed to the cause of the incident.
 - these actions will implement corrective and preventative measures.
- review and update the PIRMP one month following an incident.

The licensee will make all reasonable inquiries in relation to the incident and supply the required report to the EPA within seven days of the initial incident verbal notification.





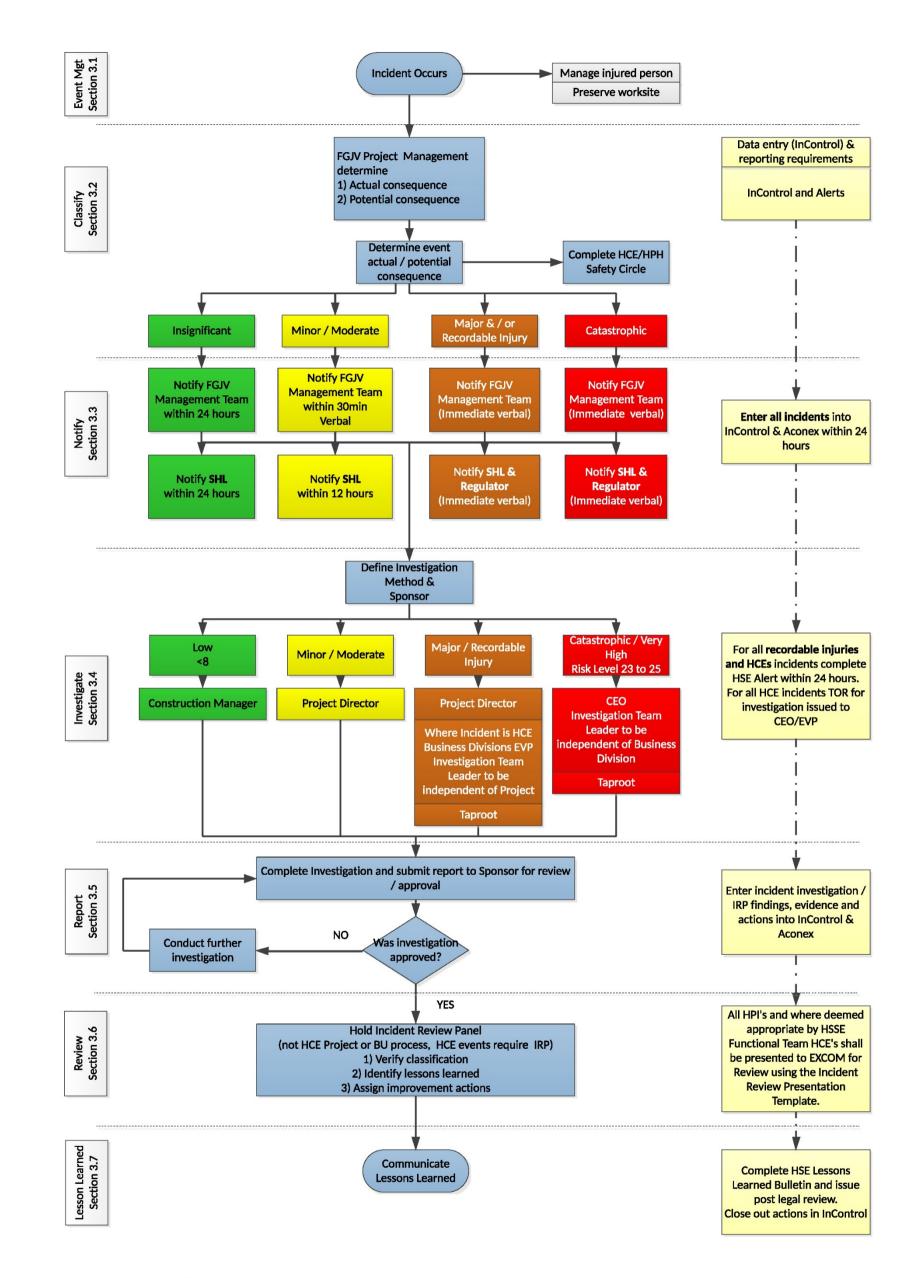


Figure 11-1: Incident Response Process

S2-FGJV-ENV-PLN-0091–Main Works Pollution Incident Response Management Plan | Page 24 of 62





12. TRAINING

Training programs on the project are set out in Section 5 of the EMS and include:

- Site Induction: All personnel (including sub-contractors) will be required to attend a compulsory site induction that includes an environmental component prior to commencement on-site. The induction is done to ensure all personnel involved in the project are aware of project requirements and to ensure the implementation of environmental management measures, including incident response and reporting, emergency response and evacuation.
- Toolbox Talks: Toolbox talks, environmental awareness training and construction methodology briefings will be delivered by Future Generation as necessary to achieve a suitable level of workforce awareness and competence appropriate to the activities. Toolbox talks will be tailored to specific environmental issues relevant to upcoming works or previous incidents.
- Daily Pre-start Meetings: Daily pre-starts will be conducted by the Future Generation Supervisors prior to the start of work each day to inform workers of key safety, environmental and activity coordination considerations and other information that may be relevant in the performance of the day's work.

In addition to the above, training will include annual testing of this PIRMP, involving desktop simulations and practical exercises or drills, as set out in Section 14.

Training records will be retained within project files.

13. AVAILABILITY

The PIRMP will be:

- kept at the premises (i.e. Lobs Hole, Tantangara and Marica as a minimum) to which the EPL relates for the duration of the Project;
- on FGJV and Project websites (PIRMP Summary only)
- on Project document control system (Aconex)
- made available to any EPA authorised officer on request;
- provided a physical copy to any project personnel or regulator.

14. TESTING AND REVIEW

This PIRMP will be tested in accordance with the regulations whereby:

- the PIRMP will routinely tested at least once every 12 months;
- the PIRMP will be reviewed within one (1) month of any pollution incident occurring and updated based on lessons learnt from the recent incident.

The PIRMP testing is to be carried out in such a manner that the information included in the PIRMP is:

- accurate;
- up to date; and
- can be implemented in a workable and effective manner.

Usual methods of testing include undertaking desktop simulations and practical exercises or drills. Testing will cover all elements of the PIRMP, including the effectiveness of training. Table 14-1 will be progressively updated following annual testing and any incidents that occur.





A Statement of Compliance of the PIRMP will be provided to the EPA as part of the EPL 21266 Annual Return.





Table 14-1: Testing Elements Tracking

Date Tested	Reason for Testing	Personnel involved in Testing (name, role and company)	Method of Testing	Outcomes and Updates	Subsequent Plan Revision Number
25/04/2022	Annual Test	Dirk McNicoll – Lobs Hole Environmental Coordinator Morgan Pinkerton – Lobs Hole Environmental Advisor	Desktop Scenario	Overall plan satisfied the relevant requirements. Minor administrational amendments to plan required.	-
22.04.2023	Annual Test	Jima Okori – Environmental Coordinator, FGJV Jemma Vivian – Enviro Advisor, FGJV Oluwatobi Aina – Environmental Advisor, FGJV Donald Mackinnon – HSE Coordinator, FGJV	Desktop Scenario	Overall plan satisfied the relevant requirements. Minor administrational amendments to plan required.	C
02.04.2024	Annual Test	Jima Okori – Environmental Coordinator, FGJV Jemma Vivian – Enviro Coordinator, FGJV Samuel Babalola – Enviro Advisor, FGJV Ian Newton – HSE Coordinator, FGJV Drew Butters – ERT Team Coordinator Ylber Kacina – ECVT Superintendent	Desktop Scenario – Simulated Drill with all stakeholders	Overall Plan satisfied the relevant requirements. Some administration amendments to the plan required. Such as ERT response time to contain spill on the river	D





15. MAPS

Physical environmental equipment to minimise the harm of an event are shown on the SAPs which are updated over time to reflect current works being undertaken.

Maps detailing the applicable location of the premises relevant to the PIRMP are the premise maps titled 'Snowy 2.0 EPL21266 - Licensed Premise Boundary'. The premise maps relevant to this PIRMP will be the latest approved maps for Future Generation works.



APPENDIX A – COMPLIANCE MATRIX

POEO Act Legislative Requirements

_egislation	Reference	Requirement	Where addressed
rotection of the nvironment Operations ct 1997	Part 5.7A Section 153A	The holder of an environment protection licence must prepare a pollution incident response management plan that complies with this Part in relation to the activity to which the licence relates.	This plan
Part 5.7A Section 153C	A pollution incident response management plan must be in the form required by the regulations and must include the following: (a) The procedures to be followed by the holder of the relevant environment protection licence, or the occupier of the relevant premises, in notifying a pollution incident to: (i) The owners or occupiers of premises in the vicinity of the premises to which the environment protection licence or the direction under section 153B relates, and (ii) The local authority for the area in which the premises to which the environment protection licence or the direction 153B relates are located and any area affected, or potentially affected, by the pollution, and (iii) Any persons or authorities required to be notified by Part 5.7,	Section 8	
		(b) A detailed description of the action to be taken, immediately after a pollution incident, by the holder of the relevant environment protection licence, or the occupier of the relevant premises, to reduce or control any pollution,	Section 11
		(c) The procedures to be followed for co-ordinating, with the authorities or persons that have been notified, any action taken in combating the pollution caused by the incident and, in particular, the persons through whom all communications are to be made,	Section 8
		(d) Any other matter required by the regulations	This plan
	Part 5.7A Section 153D	A person who is required to prepare a pollution incident response management plan under this Part must ensure that it is kept at the premises to which the relevant environment protection licence relates, or where the relevant activity takes place, and is made available in accordance with the regulations.	Section 13
	Part 5.7A Section 153E	A person who is required to prepare a pollution incident response management plan under this Part must ensure that it is tested in accordance with the regulations	Section 14
Part 5.7A Section 153F Part 5.7 Section 14		If a pollution incident occurs in the course of an activity so that material harm to the environment (within the meaning of section 147) is caused or threatened, the person carrying on the activity must immediately implement any pollution incident response management plan in relation to the activity required by this Part.	Section 11
	Part 5.7 Section 147	 (1) For the purposes of this Part: (a) harm to the environment is material if: (i) it involves actual or potential harm to the health or safety of human beings or to ecosystems that is not trivial, or (ii) it results in actual or potential loss or property damage of an amount, or amounts in aggregate, exceeding \$10,000 (or such other amount as is prescribed by the regulations), and 	Section 1.4
		(b) loss includes the reasonable costs and expenses that would be incurred in taking all reasonable and practicable measures to prevent, mitigate or make good harm to the environment.	Section 1.4
		(2) For the purposes of this Part, it does not matter that harm to the environment is caused only in the premises where the pollution incident occurs.	Section 1.4
Part	Part 5.7 Section 148	Pollution incidents causing or threatening material harm to be notified: (1) Kinds of incidents to be notified This Part applies where a pollution incident occurs in the course of an activity so that material harm to the environment is caused or threatened.	Section 8.1
		Duty of person carrying on activity to notify (2) A person carrying on the activity must, immediately after the person becomes aware of the incident, notify each relevant authority of the incident and all relevant information about it.	Section 8
		Duty of employee engaged in carrying on activity to notify (3) A person engaged as an employee in carrying on an activity must, immediately after the person becomes aware of the incident, notify the employer of the incident and all relevant information about it. If the employer cannot be contacted, the person is required to notify each relevant authority	Section 8
		(3A) Duty of employer to notify Without limiting subsection (2), an employer who is notified of an incident under subsection (3) or who otherwise becomes aware of a pollution incident which is related to an activity of the employer, must, immediately after being notified or otherwise becoming aware of the incident, notify each relevant authority of the incident and all relevant information about it.	Section 8
		Duty of occupier of premises to notify (4) The occupier of the premises on which the incident occurs must, immediately after the occupier becomes aware of the incident, notify each relevant authority of the incident and all relevant information about it.	Section 8
		Duty on employer and occupier to ensure notification (5) An employer or an occupier of premises must take all reasonable steps to ensure that, if a pollution incident occurs in carrying on the activity of the employer or occurs on the premises, as the case may be, the persons engaged by the employer or occupier will, immediately, notify the employer or occupier of the incident and all relevant information about it.	Section 8





Legislation	Reference	Requirement	Where addressed
		Extension of duty to agents and principals	Section 8
		(6) This section extends to a person engaged in carrying on an activity as an agent for another. In that case, a reference in this section to an employee extends to such an agent and a reference to an employer extends to the principal.	
		Odour not required to be reported	Section 8
		(7) This section does not extend to a pollution incident involving only the emission of an odour.	
		(8) Meaning of "relevant authority" In this section: relevant authority means any of the following:	Section 8
		(a) the appropriate regulatory authority,	Section 8
		(b) if the EPA is not the appropriate regulatory authority—the EPA,	Section 8
		(c) if the EPA is the appropriate regulatory authoritythe local authority for the area in which the pollution incident occurs,	Section 8
		(d) the Ministry of Health,	Section 8
		(e) the WorkCover Authority,	Section 8
		(f) Fire and Rescue NSW.	Section 8
	Part 5.7 Section 149	(1) If the regulations prescribe the manner or form of notifying pollution incidents under section 148, the notification is to conform to the requirements of the regulations.	Section 8
		(2) Without limiting subsection (1), the regulations:	Section 8.2
		(a) may require that verbal notification be followed by written notification, and	
		(b) may provide that notification to a designated person or authority is taken to be notification to the relevant person or authority under section 148.	Section 8
	Part 5.7 Section 150	(1) The relevant information about a pollution incident required under section 148 consists of the following:	Section 8.3
		(a) the time, date, nature, duration and location of the incident,	Section 8.3
		(b) the location of the place where pollution is occurring or is likely to occur,	Section 8.3
		(c) the nature, the estimated quantity or volume and the concentration of any pollutants involved, if known,	Section 8.3
		(d) the circumstances in which the incident occurred (including the cause of the incident, if known),	Section 8.3
		(e) the action taken or proposed to be taken to deal with the incident and any resulting pollution or threatened pollution, if known,	Section 8.3
		(f) other information prescribed by the regulations.	Section 8.3
		(2) The information required by this section is the information known to the person notifying the incident when the notification is required to be given	Section 8.3
	Part 5.7 Section 151	(3) If the information required to be included in a notice of a pollution incident by subsection (1) (c), (d) or (e) is not known to that person when the initial notification is made but becomes known afterwards, that information must be notified in accordance with section 148 immediately after it becomes known.	Section 8.3
		(1) A person is not required to notify a pollution incident under section 148 if the person is aware that the incident has already come to the notice of each person or authority required to be notified.	Section 8.2
		(2) A person is not required to notify a pollution incident under section 148 if the incident is an ordinary result of action required to be taken to comply with an environment protection licence, an environment protection notice or other requirement of or made under this Act.	Section 8.2
	Part 5.7 Section 151A	(1) This section applies to the occupier of premises where a pollution incident has occurred in the course of an activity so that material harm to the environment is caused or threatened.	Section 8.2
		(2) The EPA may direct a person to whom this section applies to notify such other persons of the incident as the EPA requires.	Section 8.2
		(3) The direction is not required to be given in writing.	Section 8.2
		(4) The direction may specify the manner or form of notifying the pollution incident and the information that must be provided.	Section 8.2
		(5) The direction may require that an initial verbal notification be followed by written notification.	Section 8.2
		(6) A person must not fail to comply with a direction given under this section.	Section 8.2
		(7) This section does not extend to a pollution incident involving only the emission of an odour	Section 8.2
		 (8) If a direction under this section is given to a person who is carrying out an activity, is engaged as an employee in carrying out an activity, or is the employer of such a person, the obligations under this section are in addition to, and not in derogation of, the obligations under section 148 (except as provided by section 151 (1)). 	Section 8.2
OEO (General) egulation 2009	Chapter 7 Part 4 Clause 101	For the purposes of section 149 of the Act, a pollution incident that is required to be notified to the EPA under Part 5.7 of the Act is to be notified verbally to the EPA by telephoning the EPA environment line, followed by notification in writing within 7 days of the date on which the incident occurred.	Section 8
		(1) A plan is to be in written form.	This plan



Future Generation Webuild • Clough • Lane



egislation Reference		Requirement				
POEO (General) Amendment (PIRMP)	Schedule 1 Part 3A Clause 98B	(2) A plan may form part of another document that is required to be prepared under or in accordance with any other law so long as the information required to be included in the plan is readily identifiable as such in that other document				
Regulation 2012	Schedule 1 Part 3A	(1) The matters required under section 153C (d) of the Act to be included in a plan are as follows:				
	Clause 98C	(a) a description of the hazards to human health or the environment associated with the activity to which the licence relates (the relevant activity),				
		(b) the likelihood of any such hazards occurring, including details of any conditions or events that could, or would, increase that likelihood,	Section 4			
		(c) details of the pre-emptive action to be taken to minimise or prevent any risk of harm to human health or the environment arising out of the relevant activity, Sec				
		(d) an inventory of potential pollutants on the premises or used in carrying out the relevant activity, Sec. 2010				
		(e) the maximum quantity of any pollutant that is likely to be stored or held at particular locations (including underground tanks) at or on the premises to which the licence Se relates,				
		(f) a description of the safety equipment or other devices that are used to minimise the risks to human health or the environment and to contain or control a pollution incident, S				
		(g) the names, positions and 24-hour contact details of those key individuals who:	Section 3			
		(i) are responsible for activating the plan, and				
		(ii) are authorised to notify relevant authorities under section 148 of the Act, and				
		(iii) are responsible for managing the response to a pollution incident,				
		(h) the contact details of each relevant authority referred to in section 148 of the Act,	Section 8.2			
		(i) details of the mechanisms for providing early warnings and regular updates to the owners and occupiers of premises in the vicinity of the premises to which the licence relates or where the scheduled activity is carried on,	Section 5			
		(j) the arrangements for minimising the risk of harm to any persons who are on the premises or who are present where the scheduled activity is being carried on,	Section 5			
		(k) a detailed map (or set of maps) showing the location of the premises to which the licence relates, the surrounding area that is likely to be affected by a pollution incident, the location of potential pollutants on the premises and the location of any stormwater drains on the premises,	Section 15			
		(I) a detailed description of how any identified risk of harm to human health will be reduced, including (as a minimum) by means of early warnings, updates and the action to be taken during or immediately after a pollution incident to reduce that risk,				
		(m)the nature and objectives of any staff training program in relation to the plan				
		(n) the dates on which the plan has been tested and the name of the person who carried out the test,	Section 14			
		(o) the dates on which the plan is updated,	This plan, document revision history			
		(p) the manner in which the plan is to be tested and maintained.	Section 14			
	Schedule 1 Part 3A Clause 98D	(1) A plan is to be made readily available:	Section 13			
		(a) to an authorised officer on request, and	Section 13			
		(b) at the premises to which the relevant licence relates, or where the relevant activity takes place, to any person who is responsible for implementing the plan.	Section 13			
		(2) A plan is also to be made publicly available in the following manner within 14 days after it is prepared:	Section 13			
		(a) in a prominent position on a publicly accessible website of the person who is required to prepare the plan,	Section 13			
		(b) if the person does not have such a website— by providing a copy of the plan, without charge, to any person who makes a written request for a copy.	Section 13			
		(3) Subclause (2) applies only in relation to that part of a plan that includes the information required under:				
		(a) section 153C (a) of the Act, and	Section 8			
		(b) clause 98C (1) (h) and (i) or (2) (b) and (c) (as the case requires).	Section 8 and 5			
		 (4) Any personal information within the meaning of the Privacy and Personal Information Protection Act 1998 is not required to be included in a plan that is made available to any person other than a person referred to in subclause (1). 	Section 8.2			
	Schedule 1 Part 3A Clause 98E	 (1) The testing of a plan is to be carried out in such a manner as to ensure that the information included in the plan is accurate and up to date and the plan is capable of being implemented in a workable and effective manner 	Section 14			
		(2) Any such test is to be carried out: (a) routinely at least once every 12 months, and (b) within 1 month of any pollution incident occurring in the course of an activity to which the licence relates so as to assess, in the light of that incident, whether the information included in the plan is accurate and up to date and the plan is still capable of being implemented in a workable and effective manner.	Section 14			



Future Generation Webuild • Clough • Lane



EPL Requirements Relevant to this PIRMP [Note: References to EPL 21266 as subject to change upon future EPL variation]

Condition	Requirement				Where addressed			
Administrative Co	onditions							
1 What the licence	e authorises and regulates							
A.1.1	This licence authorises the ca	arrying out of the scheduled development work listed	d below at the premises listed in	A2: Main Works - Electricity Generation.				
A1.4		This licence authorises the carrying out of the scheduled activities listed below at the premises specified in A2. The activities are listed according to their scheduled activity classification, fee-based activity classification and the scale of the operation. Unless otherwise further restricted by a condition of this licence, the scale at which the activity is carried out must not exceed the maximum scale specified in this condition.						
	Scheduled Activity	Fee Based Activity	Scale					
	Electricity generation	Generation of electrical power otherwise than	> 4000 GWh annual					
A2 Promises or play	nt to which this licence applies	from coal, diesel or gas	generating capacity					
A2.1	The licence applies to the follo	owing premises.						
	Premises Details		-					
	TANTANGARA	POWER STATION TALBINGO AND						
	KOSCIUSZKO NATIONAL PAR	K AND ROCK FOREST						
	KOSCIUSZKO							
	NSW 2642							
	PREMISES DEFINED BY: SNOWY 2.0 MAIN WORKS INFO	RASTRUCTURE APPROVAL CSSI 9687 (20						
	MAY 2020): APPENDIX 1 - SCH	-						
A3 Other activities								
A3.1	This licence applies to all othe	er activities carried on at the premises, including:						
	Ancillary Activity							
	Chemical Storage							
	Concrete Batching							
	Extractive Activities							
	Process Water Treatment							
	Road Construction and Mainte	enance						
A4 Information sup	plied to the EPA							
A4.1	-	carried out in accordance with the proposal contain	ed in the licence application, ex	cept as expressly provided by a condition of this licence.				
	In this condition the reference to "the licence application" includes a reference to:							
	a) the applications for any licences (including former pollution control approvals) which this licence replaces under the Protection of the Environment Operations (Savings and Transitional) Regulation 1998; and							
	b) the licence information form provided by the licensee to the EPA to assist the EPA in connection with the							
	issuing of this licence.							
2 Discharges to Air	and Water and Applications to Lar	- d						
	and Water and Applications to Lar itoring/discharge points and areas							
			s licence for the purposes of th	e monitoring and/or the setting of limits for any application of solids or liquids to the				
P1.1	utilisation area.							





	ti- Type of Monitoring Point	Type of Discharge Point	Location Description	
fication r				
1	Groundwater Bore LOBS HOLE		Wallace Creek Bridge, labelled EPL 1 in the document titled	
	EODOTIOEE		'MWEPL_Premises_Maps_202205	
			13' (DOC22/373247)	
2	Groundwater Bore		Wallace Creek Bridge, labelled EPL	
	LOBS HOLE		2 in the document titled	
			"MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
4	Groundwater Bore		Lobs Hole Portal Access labelled	
	LOBS HOLE		EPL 4 in the document titled	
			'MWEPL_Premises_Maps_202205	
5	Surface Water		13' (DOC22/373247) Yarrangobilly River, upstream of the	
Ŭ	LOBS HOLE		exploratory tunnel and construction	
			pad, labelled EPL 5 in the document	
			titled	
			'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
6	Surface Water		Wallaces Creek, upstream of the	
Ŭ	LOBS HOLE		confluence of Yarrangobilly River	
			and Wallaces Creek, labelled EPL 6	
			in the document titled	
			'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
8	Surface Water		Yarrangobilly River, downstream of	
	LOBS HOLE		Lick Hole Gully labelled EPL 8 in the	
			document titled	
			'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
9	Surface Water		Yarrangobilly River, downstream of	
	LOBS HOLE		the accommodation camp and	
			upstream of Talbingo Reservoir	
			labelled EPL 9 in the document titled	
			'MWEPL_Premises_Maps_202205	
			13' (DOC22/373247)	
10	Surface Water TALBINGO RESERVOIR		Talbingo Reservoir, upstream of Lobs Hole STP/PWTP diffuser	
	TALBINGO RESERVOIR		outlet and water intake point.	
			Labelled EPL 10 in the document	
			titled	
			'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
11	Surface Water		Talbingo Reservoir, downstream of	
	TALBINGO RESERVOIR		Lobs Hole STP/PWTP diffuser	
			outlet. Labelled EPL 11 in the	
			document titled 'MWEPL_Premises_Maps_202205	
			13' (DOC22/373247)	
12	Surface Water		Yarrangobilly River, immediately	
	LOBS HOLE		downstream of portal pad labelled	
			EPL 12 in the document titled 'MWEPL_Premises_Maps_202205	
			13' (DOC22/373247)	
14	Surface Water		Yarrangobilly River, downstream of	
	LOBS HOLE		road construction areas labelled EPL 14 in the document titled	
			MWEPL_Premises_Maps_202205	
			13' (DOC22/373247)	
15	Surface Water		Yarrangobilly River, downstream of	
	LOBS HOLE		road construction areas labelled EPL 15 in the document titled	
			'MWEPL Premises Maps 202205	
			13' (DOC22/373247)	
16	Surface Water		Yarrangobilly River, downstream of	
	LOBS HOLE		road construction areas labelled EPL 16 in the document titled	
			'MWEPL_Premises_Maps_202205	
			13' (DOC22/373247)	




he point.



24	Surface Water LOBS HOLE	Yarrangobilly River tributary (Watercourse 2), directly downstream of road, labelled EPL 24 in the document titled 'MWEPL_Premises_Maps_202205
25	Groundwater Bore LOBS HOLE	13' (DOC22/373247)' Portal Access labelled EPL 25 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
26	Surface Water MARICA	Eucumbene River, downstream of Marica Road, labelled EPL 26 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
27	Surface Water MARICA	Eucumbene River, upstream of Marica Road, labelled EPL 27 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
28	Surface Water TANTANGARA	Tantangara Reservoir, upstream in the mouth of the Murrumbidgee River. Variable location dependent on tide and reservoir levels. Labelled EPL 28 in the document titled
29	Surface Water TANTANGARA	Tantangara Reservoir, downstream of works area and upstream of lower Murrumbidgee River, labelled as EPL 29 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
30	Surface Water TANTANGARA	Kellys Plain Creek, downstream of accommodation camp and laydown areas, labelled EPL 30 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
31	Surface Water TANTANGARA	Kellys Plain Creek, upstream of accommodation camp and laydown areas, labelled EPL 31 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
32	Surface Water TANTANGARA	Tantangara Reservoir, Tantangara Intake. Downstream of construction works, labelled EPL 32 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
33	Surface Water TANTANGARA	Murrumbidgee River, downstream of Tantangara reservoir outlet labelled EPL 33 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
34	Surface Water TANTANGARA	Nungar Creek, upstream of Tantangara Road labelled EPL 34 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
35	Surface Water TANTANGARA	Nungar Creek, downstream of Tantangara Road labelled EPL 35 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
36	Surface Water ROCK FOREST	Camerons Creek, upstream of works in Rock Forest, labelled EPL 36 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)
37	Surface Water ROCK FOREST	Camerons Creek, downstream of works in Rock Forest, labelled EPL 37 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)








38	Surface Water TANTANGARA		Tantangara Reservoir, variable location dependant on tide and reservoir levels. Between emplacement area and ancillary facilities for emplacement activities. Labelled EPL 38 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
39	Surface Water TANTANGARA		Confluence of Nungar Creek and Tantangara Reservoir, variable location dependent on tide and reservoir levels. Upstream of Tantangara construction works. Labelled EPL 39 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
40	Surface Water TANTANGARA		Confluence of the upper Murrumbidgee River and Tantangara Reservoir, variable location dependent on tide and reservoir levels. Upstream of works. Labelled EPL 40 in the document titled 'MWEPL_Premises_Maps_202205	
41	Trunk Services Water Sample TALBINGO		Lobs Hole STP/PWTP Final Effluent Quality Monitoring Point. Downstream of final treatment, prior to discharge to Talbingo Reservoir. Labelled EPL 41 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
42		Discharge to waters LOBS HOLE STP/PWTP TALBINGO	Diffuser outlet discharging into Talbingo Reservoir from Lobs Hole STP/PWTP. Labelled EPL 42 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
43	Volume outflow TALBINGO		Lobs Hole STP/PWTP Final Volume Monitoring Point. Downstream of final treatment, prior to discharge to Talbingo Reservoir. Labelled EPL 43 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
44	Volume Inflow - PWTP TALBINGO		Lobs Hole PWTP Inflow Volume Monitoring Point. Labelled EPL 44 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
45	Volume Inflow - Ex-Camp STP TALBINGO		Lobs Hole Ex-Camp STP Inflow Volume Monitoring Point. Labelled EPL 45 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
46		Discharge to waters TANTANGARA RESERVOIR	Diffuser outlet discharging into Tantangara Reservoir from Tantangara STP/PWTP labelled EPL 46 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
47	Volume Inflow - Main Camp STP TALBINGO		Talbingo Main Camp STP Inflow Monitoring Point. Labelled EPL 47 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
48	Volume Inflow STP TANTANGARA		Tantangara STP Inflow Volume Monitoring Point labelled EPL 48 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
49	Volume Inflow PWTP TANTANGARA		Tantangara PWTP Inflow Volume Monitoring Point labelled EPL 49 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	








50	Trunk Services Water Sample and Volume Outflow	Tantangara STP/PWTP final effluent quality and volume monitoring point. Downstream of	
	TANTANGARA	final treatment, prior to discharge to Tantangara reservoir labelled EPL 50 in the document titled	
51	Surface Water	'MWEPL_Premises_Maps_202205 13' (DOC22/373247) Tantangara Reservoir, downstream	
	TANTANGARA	of Tantangara STP/PWTP diffuser outlet. Labelled EPL 51 in the document titled 'MWEPL_Premises_Maps_202205 13' (DOC22/373247)	
52	Surface Water LOBS HOLE	Talbingo Reservoir, upstream of GF01 emplacement area, labelled Basin labelled GF01 - SW - SB in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
53	Surface Water LOBS HOLE	Talbingo Reservoir upstream East of GF01 emplacement area labelled GF01 - SW - USE in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
54	Surface Water LOBS HOLE	Talbingo Reservoir Upstream West of GF01 emplacement area labelled GF01 - SW - USW in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
55	Surface Water LOBS HOLE	Yarrangobilly River, Surface Water Downstream of GF01 emplacement area labelled GF01 - SW - DS in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
56	Groundwater LOBS HOLE	Ground Water Upstream East from GF01 emplacement area labelled GF01 - GW - USE in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
57	Groundwater LOBS HOLE	Ground Water Upstream West from GF01 emplacement area labelled GF01 - GW - USW in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
58	Groundwater LOBS HOLE	Ground Water Downstream from GF01 emplacement area labelled GF01 - GW - DS in 'Leachate Detection Procedure - GF01' (DOC22/650275)	
59	Surface Water TANTANGARA	Tantangara Leachate Basin labelled Tan-SW-SB1 in 'Leachate	
67	Surface Water TANTANGARA	(DOC22/798284) Nungar Creek Surface Water Downstream West from Tantangara emplacement area labelled Tan-SW-DSW in 'Leachate Detection Procedure - Tantangara' (DOC22/798284)	
68	Groundwater TANTANGARA	(Ground Water Downstream East from Tantangara emplacement area labelled Tan-GW-DSE in 'Leachate Detection Procedure - Tantangara' (DOC22/798284)	
69	Groundwater TANTANGARA	Ground Water Downstream West from Tantangara emplacement area labelled Tan-GW-DSW in 'Leachate Detection Procedure - Tantangara' (DOC22/798284)	
70	Groundwater TANTANGARA	Ground Water Upstream from Tantangara emplacement area labelled Tan-GW-US in 'Leachate Detection Procedure - Tantangara' (DOC22/798284)	
71	Surface Water MARICA	Surface water downstream from Marica emplacement area labelled MAR - SW - US in 'Leachate Detection Procedure - Marica' (DOC23/27030)	








72	Groundwater MARICA	Groundwater upstream from Marica emplacement area labelled MAR -
		GW - US in 'Leachate Detection Procedure - Marica'
		(DOC23/27030)
73	Groundwater MARICA	Groundwater downstream from Marica emplacement area labelled
		MAR - GW - DS in 'Leachate
		Detection Procedure - Marica' (DOC23/27030)
76	Surface Water ROCK	Surface water Sediment Basin 1
	FOREST	from Rock Forest emplacement area labelled RF - SW - SB1 in
		'Leachate Detection Procedure -
77	Surface water ROCK	Rock Forest' (DOC23/66885)
11	FOREST	Surface water Sediment Basin 2 from Rock Forest emplacement
		area labelled RF - SW - SB2 in
		'Leachate Detection Procedure - Rock Forest' (DOC23/66885)
78	Surface water ROCK	Surface water Sediment Basin 3
	FOREST	from Rock Forest emplacement area labelled RF - SW - SB3 in
		'Leachate Detection Procedure -
		Rock Forest' (DOC23/66885)
60	Surface Water	Tantangara Leachate Basin labelled
	TANTANGARA	Tan-SW-SB2 in 'Leachate Detection Procedure - Tantangara'
		(DOC22/798284)
61	Surface Water TANTANGARA	Tantangara Leachate Basin labelled Tan-SW-SB3 in 'Leachate
		Detection Procedure - Tantangara'
62	Surface Water	(DOC22/798284) Tantangara Leachate Basin labelled
	TANTANGARA	Tan-SW-SB4 in 'Leachate
		Detection Procedure - Tantangara' (DOC22/798284)
63	Surface Water	(DOC22/798284) Tantangara Leachate Basin labelled
	TANTANGARA	Tan-SW-SB5 in 'Leachate
		Detection Procedure - Tantangara' (DOC22/798284)
64	Surface Water	Tantangara Leachate Basin labelled
	TANTANGARA	Tan-SW-SB6 in 'Leachate Detection Procedure - Tantangara'
		(DOC22/798284)
65	Surface Water	Tantangara Leachate Basin labelled
	TANTANGARA	Tan-SW-SB7 in 'Leachate Detection Procedure - Tantangara'
		(DOC22/798284)
66	Surface Water TANTANGARA	Tantangara Leachate Basin Downstream East from Tantangara
		emplacement area labelled
79	Surface water ROCK	Surface water Sediment Basin 4
	FOREST	from Rock Forest emplacement
		area labelled RF - SW - SB4 in 'Leachate Detection Procedure -
		Rock Forest' (DOC23/66885)








66	Surface Water	Tantangara Leachate Basin
	TANTANGARA	Downstream East from Tantangara emplacement area labelled
		Tan-SW-DSE in 'Leachate Detection Procedure - Tantangara'
67	Surface Water	(DOC22/798284) Nungar Creek Surface Water
01	TANTANGARA	Downstream West from
		Tantangara emplacement area labelled Tan-SW-DSW in 'Leachate
		Detection Procedure - Tantangara' (DOC22/798284)
68	Groundwater TANTANGARA	Ground Water Downstream East from Tantangara emplacement area
		labelled Tan-GW-DSE in 'Leachate
		Detection Procedure - Tantangara' (DOC22/798284)
69	Groundwater TANTANGARA	Ground Water Downstream West from Tantangara emplacement area
		labelled Tan-GW-DSW in 'Leachate
		Detection Procedure - Tantangara' (DOC22/798284)
70	Groundwater TANTANGARA	Ground Water Upstream from Tantangara emplacement area
		labelled Tan-GW-US in 'Leachate Detection Procedure - Tantangara'
71	Surface Water MARICA	(DOC22/798284) Surface water downstream from
<i>'</i> '	Sunace Water WARIOA	Marica emplacement area labelled
		MAR - SW - US in 'Leachate Detection Procedure - Marica'
70		(DOC23/27030)
72	Groundwater MARICA	Groundwater upstream from Marica emplacement area labelled MAR -
		GW - US in 'Leachate Detection Procedure - Marica'
73	Groundwater MARICA	(DOC23/27030) Groundwater downstream from
15	Oroundwater MARICA	Marica emplacement area labelled
		MAR - GW - DS in 'Leachate Detection Procedure - Marica'
		(DOC23/27030)
80	Groundwater LICK HOLE GULLY	Lick Hole Gully groundwater monitoring upstream from Lick Hole
		Gully emplacement area. Labelled EPL80 in the document titled 'Main
04		Yard' (DOC24/247978)
81	Groundwater LICK HOLE GULLY	Lick Hole Gully groundwater monitoring downstream from Lick
		Hole Gully emplacement area. Labelled EPL81 in the document
82	Groundwater MAIN YARD	titled 'Main Yard' (DOC24/247978)
02		Main Yard groundwater monitoring upstream from Main Yard
		emplacement area. Labelled EPL82 in the document titled 'Main Yard'
83	Groundwater MAIN YARD	(DOC24/247978)) Main Yard groundwater monitoring
		downstream from Main Yard
		emplacement area. Labelled EPL83 in the document titled 'Main Yard'
84	Surface Water GF01	(DOC24/247978) GF01 leachate basin labelled F8
		Basin in the document titled 'Main Yard' (DOC24/247978)
85	Surface Water MAIN YARD	Main Yard leachate basin labelled MY07 Basin in the document titled







Condition	Require	ement		
	86	Surface Water LICK HOLE GULLY	Lick Hole Gully leachate basin labelled LHG01 Basin in the document titled 'Main Yard' (DOC24/247978)	
	87	Groundwater MAIN YARD	Main Yard groundwater monitoring downstream from Main Yard emplacement area. Labelled EPL87 in the document titled 'Main Yard Additional Locations' (DOC24/247978)	
	88	Groundwater MAIN YARD	Main Yard groundwater monitoring downstream from Main Yard emplacement area. Labelled EPL88 in the document titled 'Main Yard Additional Locations' (DOC24/247978)	
	89	Groundwater LICK HOLE GULLY	Lick Hole Gully groundwater monitoring downstream from GF01 emplacement area. Labelled EPL89 in the document titled 'Main Yard Additional Locations' (DOC24/247978)	
	90	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL90 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	91	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL91 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	91	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL91 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	92	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL92 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	93	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL93 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	94	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL94 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	95	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL95 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	96	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL96 in the document titled 'GF01 Additional Locations' (DOC24/247978)	
	97	Groundwater GF01	GF01 groundwater monitoring downstream from GF01 emplacement area. Labelled EPL97 in the document titled 'GF01 Additional Locations' (DOC24/247978)	



Where addressed
Where addressed



ondition	Requireme	ent						Where addressed
imit Conditions								
Pollution of waters								
1.1	Except as	may be expressly	provided in a	any other cor	ndition of this	licence, the licen	see must comply with section 120 of the Protection of the Environment Operations Act 1997.	
2 Concentration limits								
_2.1	For each n	nonitoring/discharg	ge point or u	tilisation are	a specified in	n the table/s below	v (by a point number), the concentration of a pollutant discharged at that point, or applied to that area, must not	
L2.2		concentration lim					s must be within the specified ranges.	
LZ.Z	Pollutant	Units of Measure	50 Percentile	90 Percentile	3DGM	100 percentile		
			concentration limit	concentration limit	concentration limit	concentration limit		
	рН	рН				6.5-8.5		
2.3	To avoid a	ny doubt, this cond	dition does n	ot authorise	the pollution	of waters by any	pollutant other than those specified in the table\s.	
		-						
∟2.4	POINT 41	or Land Concentra			\sim /			
	POINT 41	nt Units of Measure	50 Percentile	90 Percentile	3DGM	100 percentile		
	Foliuta	ents of measure	concentration		concentration	concentration		
	Electric	al microsiemens per		mme	limit	700		
	conduc							
	POINT 41,50			V A	1			
	Polluta	nt Units of Measure	concentration		3DGM concentration	100 percentile concentration		
			limit	limit	limit	limit		
	Faecal Colifor	ns units per 100		10		100		
	Nitroge	millilitres n milligrams per litre	9	0.2		2		
	(ammo	nia)						
	Nitroge (total)	n milligrams per litre	•	0.35				
	Oil and Grease		9	2		5		
	Phosph		<u>_</u>	0.1		0.3		
	(total)	ioras minigrams per litre		0.1		0.0		
	Total susper	milligrams per litre ded	9	5		10		
	solids							
	POINT 50	nt Unite con	50 D (1)	00 5	2001	100 por		
	Polluta	nt Units of Measure	concentration	concentration	concentration	100 percentile concentration		
	Electric	al microsiamone	limit .	limit	limit	limit 200		
	Electric	al microsiemens per tivity centimetre				200		
.3 volume and mass lir	nits							
_3.1	For each d	ischarge point or ι	utilisation are	ea specified b	pelow (by a p	ooint number), the	volume/mass of:	
		ischarged to wate liquids applied to						
	must not ex	ceed the volume/	/mass limit sp	pecified for th	nat discharge	e point or area.		
	Point	Unit of Measure		Volur	ne/Mass Limit			
	43,50	megalitres per day	y	4.32				
	44,45,47,48,49	e megalitres per day	v					





Condition	Requirement	Where addressed
	For each discharge point or utilisation area specified below (by a point number), the flow rate of:	
L3.2	a) liquids discharged to water; or b) solids or liquids applied to the area; must not exceed the flow rate specified by that discharge point or area.	
	Point Unit of Measurement Flow rate	
	43, 50 litres per second 50 litres per second	
4 Operating Condition	IS I	
O1 Activities must be	carried out in a competent manner	
01.1	Licensed activities must be carried out in a competent manner. This includes: a) the processing, handling, movement and storage of materials and substances used to carry out the activity; and b) the treatment, storage, processing, reprocessing, transport and disposal of waste generated by the activity.	
O2 Maintenance of pl	ant and equipment	
O2.1	All plant and equipment installed at the premises or used in connection with the licensed activity: a) must be maintained in a proper and efficient condition; and b) must be operated in a proper and efficient manner.	
O3 Dust		
O3.1	All operations and activities occurring at the premises must be carried out in a manner that minimises or prevents the emission of dust from the premises.	
O4 Waste Manageme	nt	
04.1	The licensee must assess, classify and manage any waste generated at the premises in accordance with the Waste Classification Guidelines 2014 and the Act. Waste need to be transported to a place that can lawfully accept that waste.	
O5 Other operating c	onditions	
Spoil Characterisatio	n	
O5.1	Location and geochemistry The Licensee must ensure that all samples collected for spoil characterisation are: a. representative of the material currently being extracted from the specific area of the tunnel; b. representative of the material contained in the 10m advance (currently defined block); c. is not skewed by veins; and d. corresponds to the material placed on the emplacement area.	
Spoil Treatment		
O.5.2	All treatment of spoil including but not limited to the temporary storage of spoil, and treatment of Potentially Acid Forming (PAF) material and material at risk of resulting in Acid Mine Drainage or Neutral Mine Drainage, must be undertaken in a manner that: a. achieves permanent neutralisation of the material b. prevents pollution of waters; and c. prevents contamination of land.	
O5.3	The Licensee must validate that all treated spoil material meets the requirements of condition O5.2	
Spoil Emplacement		
O5.4	All spoil material must be emplaced in a manner that minimises air flow capacity and maximises neutralisation.	
Spoil Leachate Manag	jement	
O5.5	Prior to emplacing spoil on a particular spoil emplacement area, the Licensee must develop a leachate detection system which characterises the quality of any leachate being generated from within the emplacement areas.	
O5.6	Within 2 weeks of developing the leachate detection system, the Licensee must provide a report detailing the findings and recommendations for the leachate detection system/s required by Condition O5.5 to the EPA's Manager Regulatory Operations Regional	
Spoil Management Co	-	
O5.7	The Licensee must maintain and implement a contingency plan in the event that characterisation, treatment, emplacement or leachate management does not meet the appropriate thresholds within the QAQC plan.	
5 Monitoring and Rec	ording Conditions	
M1.1	The results of any monitoring required to be conducted by this licence or a load calculation protocol must be recorded and retained as set out in this condition.	





Condition	Requirement	Where addressed
M1.2	All records required to be kept by this licence must be:	
	(a) in a legible form, or in a form that can readily be reduced to a legible form;	
	(b) kept for at least 4 years after the monitoring or event to which they relate took place; and	
	(c) produced in a legible form to any authorised officer of the EPA who asks to see them.	
M1.3	The following records must be kept in respect of any samples required to be collected for the purposes of this licence:	
	(a) the date(s) on which the sample was taken;	
	(b) the time(s) at which the sample was collected;	
	(c) the point at which the sample was taken; and	
	(d) the name of the person who collected the sample.	
M2 Requirement to	monitor concentration of pollutants discharged	
M2.1	For each monitoring/discharge point or utilisation area specified below (by a point number), the licensee must monitor (by sampling and obtaining results by analysis) the concentration of each pollutant specified in Column 1. The licensee must use the sampling method, units of measure, and sample at the frequency, specified opposite in the other columns:	





M2.2

Water and/ Land Monitoring Requirements

POINT 1,2,4,25

Pollutant	Units of measure	Frequency	Sampling Method
Aluminium (dissolved)	micrograms per litre	Quarterly	Grab sample
Copper (dissolved)	micrograms per litre	Quarterly	Grab sample
Dissolved Oxygen	percent saturation	Quarterly	Grab sample
Electrical conductivity	microsiemens per centimetre	Quarterly	Grab sample
Iron (dissolved)	micrograms per litre	Quarterly	Grab sample
Lead (dissolved)	micrograms per litre	Quarterly	Grab sample
Manganese (dissolved)	micrograms per litre	Quarterly	Grab sample
Nickel (dissolved)	micrograms per litre	Quarterly	Grab sample
Nitrogen (total)	micrograms per litre	Quarterly	Grab sample
Oxidation Reduction Potential	millivolts	Quarterly	Grab sample
Reactive Phosphorus	micrograms per litre	Quarterly	Grab sample
Silver (dissolved)	micrograms per litre	Quarterly	Grab sample
Turbidity	nephelometric turbidity units	Quarterly	Grab sample
Zinc (dissolved)	micrograms per litre	Quarterly	Grab sample

POINT 5,6,8,9,10,11,12,14,15,16,24,26,27,28,29,30,31,32,33,34,35,36,37,38,39,40,41,50,51,52,53,54,5 5,56,57,58,59,60,61,62,63,64,65,66,67,68,69,70,71,72,73,76,77,78,79,80,81,82,83,84,85,86,87,8 8,89,90,91,92,93,94,95,96,97

Pollutant	Units of measure	Frequency	Sampling Method
Aluminium (dissolved)	milligrams per litre	Monthly	Grab sample
Copper (dissolved)	micrograms per litre	Monthly	Grab sample
Iron (dissolved)	micrograms per litre	Monthly	Grab sample
Lead (dissolved)	micrograms per litre	Monthly	Grab sample
Manganese (dissolved)	micrograms per litre	Monthly	Grab sample
Nickel (dissolved)	micrograms per litre	Monthly	Grab sample
Nitrogen (total)	micrograms per litre	Monthly	Grab sample
Reactive Phosphorus	micrograms per litre	Monthly	Grab sample
Silver (dissolved)	micrograms per litre	Monthly	Grab sample
Zinc (dissolved)	micrograms per litre	Monthly	Grab sample

POINT 5,6,8,9,10,11,12,14,15,16,24,26,27,28,29,30,31,32,33,34,35,36,37,38,39,40,41,50,51,52,53,54,5 5,56,57,58,59,60,61,62,63,64,65,66,67,68,69,70,71,76,77,78,79,80,81,82,83,84,85,86,87,88,89,9 0,91,92,93,94,95,96,97


Pollutant	Units of measure	Frequency	Sampling Method
Arsenic (dissolved)	micrograms per litre	Monthly	Grab sample
Chromium (dissolved)	micrograms per litre	Monthly	Grab sample
Cyanide (total)	micrograms per litre	Monthly	Grab sample
Hardness (as calcium carbonate)	milligrams per litre	Monthly	Grab sample
Oil and Grease	milligrams per litre	Monthly	Grab sample
Phosphorus (total)	micrograms per litre	Monthly	Grab sample
Total Kjeldahl Nitrogen	micrograms per litre	Monthly	Grab sample

POINT 5,6,8,9,10,11,12,14,15,16,24,26,27,28,29,30,31,32,33,34,35,36,37,38,39,40,41,50,51,52,53,54,5 5,56,57,58,59,60,61,62,63,64,65,66,67,68,69,70,71,76,77,78,79

Pollutant	Units of measure	Frequency	Sampling Method
Arsenic (dissolved)	micrograms per litre	Monthly	Grab sample
Chromium (dissolved)	micrograms per litre	Monthly	Grab sample
Cyanide (total)	micrograms per litre	Monthly	Grab sample
Hardness (as calcium carbonate)	milligrams per litre	Monthly	Grab sample
Dil and Grease	milligrams per litre	Monthly	Grab sample
Phosphorus (total)	micrograms per litre	Monthly	Grab sample
Total Kjeldahl Nitrogen	micrograms per litre	Monthly	Grab sample

POINT 5,6,8,9,10,11,12,14,15,16,24,26,27,28,29,30,31,32,33,34,35,36,37,38,39,40,41,50,51,52,53,54,5 5,59,60,61,62,63,64,65,66,67,71,76,77







			_	
	Pollutant	Units of measure	Frequency	Sampling Method
	Electrical conductivity	microsiemens per	Monthly	In situ
	pH	centimetre pH	Monthly	In situ
	Total suspended	milligrams per litre	Monthly	Grab sample
	solids			
		5,16,24,26,27,28,29,30,31,32, 55,66,67,71,76,77,80,81,82,83		
	Pollutant	Units of measure	Frequency	Sampling Method
	Ammonia	micrograms per litre	Monthly	Grab sample
		5,16,24,26,27,28,29,30,31,32, 90,91,92,93,94,95,96,97	33,34,35,36,37,38,39	,40,41,50,51,80,81,82,8
	Pollutant	Units of measure	Frequency	Sampling Method
	Oxidised nitrogen	micrograms per litre	Monthly	Grab sample
	5,6,8,9,10,11,12,14,1 1,62,63,64,65,66,67,7	5,16,24,26,27,28,29,30,31,32, 71,76,77,78,79	33,34,35,36,37,38,39	,40,52,53,54,55,59,60,6
	Pollutant	Units of measure	Frequency	Sampling Method
	Oxidation Reduction Potential	millivolts	Monthly	In situ
	Temperature	degrees Celsius	Monthly	In situ
	1,62,63,64,65,66,67,7	5,16,24,26,27,28,29,30,31,32, 71,76,77,78,79,84,85,86	33,34,35,36,37,38,39	
	Pollutant	Units of measure	Frequency	Sampling Method
		percept exturation	Monthly	In situ
	Dissolved Oxygen	percent saturation		
	Dissolved Oxygen Turbidity	nephelometric turbidity units	Monthly	In situ
DINT	Turbidity 10,11,28,41,50,51	nephelometric turbidity units	Monthly	In situ
OINT	Turbidity 10,11,28,41,50,51 Pollutant	nephelometric turbidity units Units of measure	Monthly Frequency	In situ Sampling Method
DINT	Turbidity 10,11,28,41,50,51 Pollutant BOD	nephelometric turbidity units Units of measure milligrams per litre	Monthly Frequency Monthly	In situ Sampling Method Grab sample
OINT	Turbidity 10,11,28,41,50,51 Pollutant	nephelometric turbidity units Units of measure	Monthly Frequency	In situ Sampling Method
OINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms	nephelometric turbidity units Units of measure milligrams per litre colony forming units per 100 millilitres 60,61,62,63,64,65,66,67,71,7	Monthly Frequency Monthly Monthly	In situ Sampling Method Grab sample Grab sample
OINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59	nephelometric turbidity units Units of measure milligrams per litre colony forming units per 100 millilitres 60,61,62,63,64,65,66,67,71,7	Monthly Frequency Monthly Monthly	In situ Sampling Method Grab sample Grab sample
OINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59 91,92,93,94,95,96,97	Units of measure milligrams per litre colony forming units per 100 millilitres ,60,61,62,63,64,65,66,67,71,7	Monthly Frequency Monthly Monthly 6,77,78,79,80,81,82,8	In situ Sampling Method Grab sample Grab sample 33,84,85,86,87,88,89,90,
POINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59 91,92,93,94,95,96,97 Pollutant Nitrate + nitrite (oxidised nitrogen)	Units of measure milligrams per litre colony forming units per 100 millilitres ,60,61,62,63,64,65,66,67,71,7 Units of measure	Monthly Frequency Monthly Monthly 6,77,78,79,80,81,82,8 Frequency Monthly	In situ Sampling Method Grab sample Grab sample 33,84,85,86,87,88,89,90, Sampling Method
OINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59 91,92,93,94,95,96,97 Pollutant Nitrate + nitrite (oxidised nitrogen)	nephelometric turbidity units Units of measure milligrams per litre colony forming units per 100 millilitres ,60,61,62,63,64,65,66,67,71,7 Units of measure micrograms per litre	Monthly Frequency Monthly Monthly 6,77,78,79,80,81,82,8 Frequency Monthly	In situ Sampling Method Grab sample Grab sample 33,84,85,86,87,88,89,90, Sampling Method
OINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59 91,92,93,94,95,96,97 Pollutant Nitrate + nitrite (oxidised nitrogen) 52,53,54,55,56,57,58 Pollutant Arsenic (total)	nephelometric turbidity units Units of measure milligrams per litre colony forming units per 100 millilitres ,60,61,62,63,64,65,66,67,71,7 Units of measure micrograms per litre ,59,60,61,62,63,64,65,66,67,6 Units of measure micrograms per litre	Monthly Frequency Monthly Monthly 6,77,78,79,80,81,82,8 Frequency Monthly 8,69,70 Frequency Monthly	In situ Sampling Method Grab sample Grab sample 33,84,85,86,87,88,89,90, Sampling Method Grab sample Sampling Method Grab sample
POINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59 91,92,93,94,95,96,97 Pollutant Nitrate + nitrite (oxidised nitrogen) 52,53,54,55,56,57,58 Pollutant Arsenic (total) Chromium (total)	nephelometric turbidity units Units of measure milligrams per litre colony forming units per 100 millilitres ,60,61,62,63,64,65,66,67,71,7 Units of measure micrograms per litre ,59,60,61,62,63,64,65,66,67,6 Units of measure micrograms per litre micrograms per litre micrograms per litre	Monthly Frequency Monthly Monthly Monthly 6,77,78,79,80,81,82,8 Frequency Monthly 8,69,70 Frequency Monthly Monthly Monthly	In situ Sampling Method Grab sample Grab sample 33,84,85,86,87,88,89,90, Sampling Method Grab sample Sampling Method Grab sample Grab sample Grab sample
POINT	Turbidity 10,11,28,41,50,51 Pollutant BOD Faecal Coliforms 36,37,52,53,54,55,59 91,92,93,94,95,96,97 Pollutant Nitrate + nitrite (oxidised nitrogen) 52,53,54,55,56,57,58 Pollutant Arsenic (total)	nephelometric turbidity units Units of measure milligrams per litre colony forming units per 100 millilitres ,60,61,62,63,64,65,66,67,71,7 Units of measure micrograms per litre ,59,60,61,62,63,64,65,66,67,6 Units of measure micrograms per litre	Monthly Frequency Monthly Monthly 6,77,78,79,80,81,82,8 Frequency Monthly 8,69,70 Frequency Monthly	In situ Sampling Method Grab sample Grab sample 33,84,85,86,87,88,89,90, Sampling Method Grab sample Sampling Method Grab sample

Monthly

Monthly

Monthly

Monthly

Grab sample

Grab sample

Grab sample

Grab sample

Nickel (total)

Silver (total)

Total Iron


micrograms per litre

micrograms per litre

Total manganese micrograms per litre

micrograms per litre







Condition	Requirement							
	Zinc (total)	micrograms per litre	Monthly	Grab sample				
	POINT 52,53,54,55,56,57,	58,59,60,61,62,63,64,65,66,67,	68,69,70,72,73					
	Pollutant	Units of measure	Frequency	Sampling Method				
	Aluminium (total)	micrograms per litre	Monthly	Grab sample				
	POINT 56,57,58,68,69,70,	72,73	/	\sim \sim $>$				
	Pollutant	Units of measure	Frequency	Sampling Method	-			
	Dissolved Oxygen	percent saturation	Monthly	Grab sample				
	Electrical conductivity Oxidation Reduction	microsiemens per centimetre n millivolts	Monthly Monthly	Grab sample Grab sample				
	Potential pH	pН	Monthly	Grab sample				
	Temperature	degrees Celsius	Monthly	Grab sample				
	Turbidity	nephelometric turbidity units	Monthly	Grab sample				
M3 Testing metho	ds - concentration limits							
M3.1	Approved Methods	s Publication unless ar	nother method	has been approved by th	EPA in writing before any		r applied to a utilisation area m	nust be done in acco
M3.2		so applies to the monit	oring of any po	ints identified in Condition	i IVIZ.Z			
M4 Recording of p	collution complaints							
M4.1	The licensee must	keep a legible record	of all complaint	s made to the licensee of	any employee or agent of	the licensee in relation to	o pollution arising from any act	tivity to which this lic
M4.2	The record must in	clude details of the fol	lowing:					
	(a) the date a	and time of the compla	aint;					
	(b) the method	od by which the compl	aint was made	,				
	(c) any perso	onal details of the com	plainant which	were provided by the co	nplainant or, if no such deta	ils were provided, a note	e to that effect;	
	(d) the nature	e of the complaint;						
	(e) the action	n taken by the licensee	e in relation to t	he complaint, including a	ny follow-up contact with the	e complainant; and		
	(f) if no actio	on was taken by the lic	ensee, the rea	sons why no action was	aken.			
M4.3	The record of a cor	mplaint must be kept f	or at least 4 ye	ars after the complaint w	s made.			
M4.4	The record must be	e produced to any auth	norised officer of	of the EPA who asks to s	e them.			
M5 Telephone cor	nplaints line							
M5.1						ving any complaints fron	n members of the public in re	lation to activities c
M5.2		· · · · · · · · · · · · · · · · · · ·		wise specified in the lice telephone number and		Its line so that the impac	ted community knows how to	make a complaint.
M5.2 M5.3		· ·	•	•	•	·		
			iy unui immedia	ately the date of the issue				
M6 Requirement t	o Monitor volume or mass		.6. 11		••			
M6.1		e point or utilisation ar quids discharged to wa		elow, the licensee must n to the area:	onitor:			
		ids applied to the area						
	c) the mass of poll	utants emitted to the a	air;					
		nd using the method a	ind units of mea	asure, specified below.				
	POINT 43,50		2					
	Frequency Continuous	Unit of Measure megalitres per day	Sampling Me					
	POINT 44,45,47,48,49 Frequency	Unit of Measure	Sampling Me	athod				
	Continuous	megalitres per day	Ultrasonic flo					
6. Reporting Con	ditions							
	The licensee must							
R1.1		complete and supply t	to the EPA an A	Annual Return in the app	oved form comprising:			



	Where addressed
accordance with the	
nis licence applies.	
ies conducted at the	
aint.	
	Section 15



Condition	Requirement	Where addressed
R2.1	Notifications must be made by telephoning the Environment Line service on 131 555. Note: The licensee or its employees must notify all relevant authorities of incidents causing or threatening material harm to the environment immediately after the person becomes aware of the incident in accordance with the requirements of Part 5.7 of the Act.	Section 9.2
R2.2	The licensee must provide written details of the notification to the EPA within 7 days of the date on which the incident occurred.	Section 9.2
	Where an authorised officer of the EPA suspects on reasonable grounds that:	Section 9.2
R3.1	a) where this licence applies to premises, an event has occurred at the premises; or	Section 9.2
	Notifications must be made by telephoning the Environment Line service on 131 555. Sector Note: The licensee or its employees must notify all relevant authorities of incidents causing or threatening material harm to the environment immediately after the person becomes aware of the incident in accordance with the requirements of Part 5.7 of the Act. Sector The licensee must provide written details of the notification to the EPA within 7 days of the date on which the incident occurred. Sector Where an authorised officer of the EPA suspects on reasonable grounds that: Sector a) where this licence applies to premises, an event has occurred on the socurred on or off premises to which the licence applies), the authorised officer may request a written report of the event. Sector b) where this licence applies to vehicles or mobiling or nobiling information: Sector 12 The request may require a report which includes any or all of the following information: Sector a) the pays, thine and duration of the event; Sector b) the type, volume and concentration of every pollutant discharged as a result of the licensee, is aware) who witnessed the event; Sector c) the name, address and business hours telephone number of employees or agents of the licensee is aware) who witnessed the event; Sector c) the name, address and business hours telephone number of every other person (of whom the licensee is aware) who witnessed the event; Sector	Section 9.2
R3.2	The licensee must make all reasonable inquiries in relation to the event and supply the report to the EPA within such time as may be specified in the request.	Section 9.2 and Sectio 12
	The request may require a report which includes any or all of the following information:	Section 9.2
	a) the cause, time and duration of the event;	Section 9.2
	b) the type, volume and concentration of every pollutant discharged as a result of the event;	Section 9.2
	c) the name, address and business hours telephone number of employees or agents of the licensee, or a specified class of them, who witnessed the event;	Section 9.2
R3.3		Section 9.2
	e) action taken by the licensee in relation to the event, including any follow-up contact with any complainants;	Section 9.2
	f) details of any measure taken or proposed to be taken to prevent or mitigate against a recurrence of such an event; and	Section 9.2
	g) any other relevant matters	Section 9.2
R3.4		Section 9.2
R4 Other reporting	conditions	
R4.1	The licensee must notify the EPA within 24 hours by phone or in writing of:	Section 9.2
	6.1.2 of the Water Management Plan- Snowy 2.0 Main Works and the Australian and New Zealand Environment Conservation Council Guidelines	Section 9.2
	the Water Management Plan - Snowy 2.0 Main Works and the Australian and New Zealand Environment Conservation Council Guidelines	Section 9.2
Environmental Mor	• .	
R4.2		
R4.3		
R4.4	a) results of all water quality monitoring undertaken in the relevant preceding period nominated in Condition R4.2	
	b) results of all weather monitoring undertaken in the relevant preceding period nominated in Condition R4.2 and R4.3;	
	 d) identification of instances where the water quality objective triggers for each relevant pollutant were exceeded at receiving water locations and/or where the predicted discharge water quality was exceeded at sediment basin discharge points; e) include details of any actions taken by the Licensee in response to exceedances identified under point (d), including but not limited to: additional monitoring remedial actions; and iii. activation of trigger, action, response plans (TARPs); f) recommendations for future actions in relation to monitoring and/or management 	



Future Generation Webuild • Clough • Lane



Condition	Requirement
R4.5	 For each emplacement area (Main Yard, GF01, Tantangara, Rock Forest, Marica and Ravine Bay), the Licensee must provide a quarterly spoil monitoring report (The Spoil Monitoring Report). The Spoil Monitoring Report must be provided by: 1. 30 April each year for Quarter 1 of the calendar year (1 January - 31 March) 2. 31 July each year for Quarter 2 of the calendar year (1 April - 30 June) 3. 31 October each year for Quarter 3 of the calendar year (1 July - 30 September) 4. 31 January each year for Quarter 4 of the calendar year (1 October - 31 December)
R4.6	The Spoil Monitoring Report must be prepared by a suitably qualified and experienced person and include, but need not be limited to: a) Quantities of spoil that has been emplaced (in m3) b) Results of all spoil characterisation that has occurred in the quarter. Including but not limited to quantities of: i. Non-acid forming material (NAF) ii. Acid neutralisation capacity material (ANC) iii. Potentially acid forming material (PAF) iv. Any other relevant spoil streams c) Treatment undertaken on the emplaced spoil following the characterisation d) Proof of validation of all treated spoil e) Cumulative total volumes of spoil emplaced, including but not limited to: i. Non-acid forming material (NAF) iii. Potentially acid forming material (NARC) iii. Transporting spoil of spoil. This may include but need not be limited to: i. Additional treatment undertaken prior to emplacement iii. Additional controls undertaken prior to emplacement iii. Transporting spoil offsite to a lawful facility iv. Any other remedial acidons g) Leachate generated from the spoil emplacement area. This should include, but need not be limited to: i. Volumes of leachate generated iii. Quality of leachate generated iii. Acuality of leachate ge
R4.7	The Spoil Monitoring Report must identify if any emplacement area nominated under Condition R4.5 has not had any spoil emplacement in the relevant quarter (i.e. emplacement commenced, has not occurred in the quarter or the emplacement has ceased in that area).
8 Pollution studies an	Ind Reduction Programs
U1 Diffuse Source Wa	ater Pollution Management
U1.1	By 31 March 2023, the licensee must implement the recommended action and controls for item numbers 1, 2, 3, 4, 8 and 32 outlined in the report titled "Assessment of Diffuse Source Management - Snowy 2.0 Project." (DOC23/27477).
U1.2	By 14 April 2023, the licensee must provide a written report to the EPA's Manager Regulatory Operations - Regional South detailing the completion of the works outlined in Condition I
U1.3	By 30 June 2023, the licensee must implement the recommended action and controls for item numbers 7, 9, 10, 12, 26 and 28 outlined in the report titled "Assessment of Diffuse Pollution Management - Snowy 2.0 Project." (DOC23/27477).
U1.4	By 14 July 2023, the licensee must provide a written report to the EPA's Manager Regulatory Operations - Regional South detailing the completion of the works outlined in condition U
U1.5	By 31 December 2023, the licensee must implement the recommended action and controls for item numbers 5 and 25 outlined in the report titled "Assessment of Diffuse Source V Management - Snowy 2.0 Project." (DOC23/27477).
U1.6	By 14 January 2024, the licensee must provide a written report to the EPA's Manager Regulatory Operations - Regional South detailing the completion of the works outline in condition
U2 Generator emissio	on improvements program
U2.1	Licensee must complete the outstanding program of works relating to electrical generators used across the Premises to achieve compliance with the Protection of the Environment Operation 2021 (the Clean Air Regulation). The program may include, but need not be limited to: 1. Improving current emissions standards from electrical generators used across the Premises to achieve compliance with the Clean Air Regulation, or 2. Decommissioning electrical generators used across the Premises that are unable to achieve compliance with the Clean Air Regulation Note: Condition U2.1 relates to 1 unit at Marica that an SCR unit is required for and the installation of emission reduction units for 10 smaller generators across all main work sites.



	Where addressed
acement has not yet	
ource Water Pollution	
dition U1.1 above.	
iffuse Source Water	
tion U1.3 above.	
urce Water Pollution	
ndition U1.5 above.	
nt Operations (Clean	
es.	



J2.2 E1 Verification of mixi	By [date to be specified by licensee] the Licensee must provide a report to the Manager Regulatory Operations Regional South detailing completion of Condition U2.1
	ing zone modelling
	ing Lono modoling
E1.1	The licensee must engage a suitably qualified and experienced person(s) to prepare a Mixing Zone Verification Program.
E1.2	At least 4 weeks prior to the first discharge of each of the sewage treatment plants and process water treatment plants, the licensee must submit a written plan for the Mixing Zone Verification Program must include, but need not be limited to: a. Sampling locations Sampling locations must be comparable to the key locations identified in <i>Attachment F Waste and Process Water Mixing Zone Assessment</i> (7 February 2020) of the "Snowy 2.0 Response to Submissions Main Report - Appendix J Revised Water Management Report" and capture ambient water quality;
	b. Sampling frequency and duration The frequency and duration of sampling must be adequate to capture the full range of receiving waterway conditions, including but not limited to, winds, current, temperature and modelling predictions under a range of scenarios to be verified;
	c. Sampling depth Sampling must allow for variations at depth under a range of scenarios (i.e. thermal stratification); and
	 d. Sampling parameters The parameters must include, but need not be limited to: i. Total nitrogen; ii. Total phosphorus; iii. pH; iv. Biological Oxygen Demand; v. Nitrogen (ammonia); vi. Turbidity; and vii. Electrical Conductivity.
E1.3	Within 6 weeks of the first discharge from each sewage treatment plant and the process water treatment plants, the licensee must submit a written progress report for the Mixing Z Program to the EPA's Manager Regulatory Operations.
E1.4	Upon completion of the Mixing Zone Verification Program (as per Condition E1.2 (b)), the licensee must submit a written final report detailing the results of the Mixing Zone Verification each of the sewage treatment plants and process water treatment plants to the EPA's Manager Regulatory Operations – Regional South.
E1.5	The written progress report and final reports referred to in Condition E1.3 and E1.4 above must include, but need not be limited to: a. a statement of the ambient NSW Water Quality Objectives (WQOs) of the receiving waters (Talbingo/Tantangara Reservoir) relevant to the discharge, including the associated guideline values or criteria for the identified environmental values;
	b. a description of the ambient water quality of Talbingo/Tantangara Reservoir in relation to the relevant WQOs, to determine whether the WQOs are being achieved;
	c. ambient conditions (e.g. currents, temperature, density, storage level and thermal stratification processes);
	 d. discharge and release conditions including but not limited to: i. rate of discharge; ii. timing; iii. total volume; iv. water quality of discharge;
	e. a description of the mixing zone, including the extent and shape of the mixing zone;
	f. a comparison of point e. above with the modelled predications from Attachment F Waste and Process Water Mixing Zone Assessment (7 February 2020) of the "Snowy 2.0 - Main We to Submissions Main Report - Appendix J Revised Water Management Report" including discussion of the mixing zone modelling and whether the relevant guideline values are being of the near-field mixing zone; and
	g. a continuous improvement plan for managing wastewater discharge over time, so as to reduce the extent and impact of the mixing zone
	Note: This program has been developed to verify the modelled water quality impacts on the Talbingo and Tantangara reservoir of the proposed discharge of treated effluent from the se and process water treatment plants. The EPA intends to use this information to refine discharge criteria in this licence.
-2 Correlation Assess	ment – Faecal Coliforms



	Where addressed
erification Program	
2.0 - Main Works -	
nd rainfall, to allow	
g Zone Verification	
cation Program for	
ted indicators and	
<i>Works - Response</i> ng met at the edge	
sewage treatment	



Condition	Requirement	Where addressed
E2.1	The Licensee is permitted to undertake an assessment to trial the use of a membrane filtration method (in-field) for monitoring of faecal coliforms in the field. The assessment must: 1. Ensure that the in-field and laboratory samples are taken concurrently over a period of time that is sufficient to derive a statistically robust correlation between methods. Samples may be taken more frequently than the licence requires in order to achieve this if desired 2. Derive a statistical correlation between the membrane filtration method and the method currently used in compliance with the Approved Methods Publication 3. Ensure that appropriate quality control procedures are followed 4. Demonstrate the accuracy and reliability of the membrane filtration method; and 5. Provide recommendations on an appropriate frequency of monitoring for the membrane filtration method	
E2.2	The Licensee must provide a written report detailing compliance with the above requirements to the Manager Regulatory Operations Regional South following completion of the assessment.	





APPENDIX B – ENVIRONMENTAL ASPECTS AND IMPACTS REGISTER

No	A odivišta	Environmental	Risk	Course	Dessible Outcome	Concernance	Likelihaad	Initial	Diak Tractmont(a)	Concernation	Likeliheed	Residual	Risk
NO	Activity	Aspect	RISK	Cause	Possible Outcome	Consequence	Likelihood	Risk Rating	Risk Treatment(s)	Consequence	Likelihood	Risk Rating	Owner
1	Vegetation Clearing	Biodiversity	Injury/mortality of fauna	Removal of occupied habitat, including hollow- bearing trees, shrubs, nests, ground cover, rocks	- Reputational impacts - Potential regulatory action from agencies	3 - Moderate	4 - Likely	12 - High	 Biodiversity Management Plan Pre-clearing procedure Ecologists supervision during clearing operations 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
2	Vegetation Clearing	Biodiversity	Removal of vegetation/habitat not permitted to be impacted by the project approval	Vegetation clearing outside of construction envelope	 Unauthorised impact to flora / National Park Project delays Financial penalties Reputational impacts 	4 - Major	3 - Possible	12 - High	 Biodiversity Management Plan Exclusion zones and defined clearing limits and no-go zones Training of contractors on environmental exclusion zones and consequences Sensitive Area Plans / GIS mapping 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
3	Vegetation Clearing	Biodiversity	Removal of vegetation/habitat not permitted to be impacted by the project approval	Vegetation clearing that results in impacts additional to the total area in condition 5 of schedule 2	- Unauthorised impact to flora / National Park - Project delays - Financial penalties - Reputational impacts	4 - Major	3 - Possible	12 - High	 Biodiversity Management Plan Exclusion zones, defined clearing limits and no- go zones Training of contractors on environmental exclusion zones and consequences Sensitive Area Plans / GIS mapping 	3 - Moderate	2 - Unlikely	6 - Medium	Snowy Hydro
4	Earthworks/ Roadworks	Biodiversity	Removal of vegetation/habitat not permitted to be impacted by the project approval	Vegetation clearing outside of construction envelope	- Unauthorised impact to flora / National Park - Project delays - Financial penalties - Reputational impacts	4 - Major	3 - Possible	12 - High	 Biodiversity Management Plan Spoil Management Plan Exclusion zones and defined clearing limits and no-go zones Training of contractors on environmental exclusion zones Sensitive Area Plans / GIS mapping 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
5	Earthworks/ Roadworks	Biodiversity	Impacts on vegetation/habitat beyond the construction envelope	Improper stockpiling of excavated material and engineered fill	 Unapproved impacts beyond construction envelope Potential regulatory action from agencies Project delays Financial penalties Reputational impacts 	3 - Moderate	3 - Possible	9 - Medium	- Spoil Management Plan - Biodiversity Management Plan - Training of contractors on environmental exclusion zones - Sensitive Area Plans / GIS mapping	3 - Moderate	1 - Rare	3 - Low	Future Generation
6	Construction of waterway crossings	Biodiversity	Loss of aquatic habitat not permitted to be impacted by the construction envelope	Clearing outside the project footprint, plant operation and excavation outside project footprint	 Unapproved impacts beyond construction envelope Potential regulatory action from agencies Reputational impacts 	3 - Moderate	3 - Possible	9 - Medium	 Biodiversity Management Plan Exclusion zones and defined clearing limits and no-go zones Training of contractors on environmental exclusion zones and consequences Sensitive Area Plans / GIS mapping 	3 - Moderate	1 - Rare	3 - Low	Future Generation
7	Construction of waterway crossings	Biodiversity	Injury/mortality of aquatic fauna	Earthworks/clearing and construction at waterway crossings without proper ecological supervision and procedures.	- Unauthorised impact to fauna (and potentially threatened fauna) - Potential regulatory action from agencies	3 - Moderate	3 - Possible	9 - Medium	 Biodiversity Management Plan Pre-clearance procedure Ecologist supervision during clearing Exclusion zones and defined clearing limits and no-go zones Training of contractors on environmental exclusion zones and consequences Sensitive Area Plans / GIS mapping 	2 - Minor	2 - Unlikely	4 - Low	Future Generation
8	Construction of Barge Access Infrastructure	Biodiversity	Injury/mortality of aquatic fauna	Earthworks/Clearing in riparian habitats adjacent to the Talbingo Reservoir	 Unauthorised impact to fauna (and potentially threatened fauna) Potential regulatory action from agencies 	3 - Moderate	3 - Possible	9 - Medium	- Biodiversity Management Plan	2 - Minor	2 - Unlikely	4 - Low	Future Generation
9	Construction of Barge Access Infrastructure	Biodiversity	Loss of aquatic habitat not permitted to be impacted by the project approval	Earthworks/Construction within Talbingo Reservoir beyond the approved construction envelope	 Unauthorised impact to fauna (and potentially threatened fauna) Unapproved impacts beyond construction envelope Potential regulatory action from agencies 	3 - Moderate	3 - Possible	9 - Medium	- Biodiversity Management Plan - Training for contractors - Sensitive Area Plans / GIS mapping	3 - Moderate	1 - Rare	3 - Low	Future Generation
10	Dredging	Biodiversity	Loss of fish, fish eggs and invertebrates within the dredge area	Hydraulic entrainment of aquatic fauna in the dredge cutter head	 Unauthorised impact to fauna (and potentially threatened fauna) Impacts to aquatic fauna population Loss of threatened species within Talbingo Reservoir 	3 - Moderate	3 - Possible	9 - Medium	- Dredging Management Plan (for Exploratory Works if required)	4 - Major	1 - Rare	4 - Low	Future Generation
11	Stockpile/spoil emplacement	Biodiversity	Introduction and spread of weeds, pests and pathogens causing	Disturbance of natural areas and storage of spoil provides opportunity for weeds to establish and	 Impact to biodiversity in exceedance of the approved Project Spread of weeds in the National Park Smothering / impacts to native 	3 - Moderate	4 - Likely	12 - High	- Biodiversity Management Plan - Weed, Pest and Pathogen Management Plan	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation





								Initial				Residual	
No	Activity	Environmental Aspect	Risk	Cause	Possible Outcome	Consequence	Likelihood	Risk Rating	Risk Treatment(s)	Consequence	Likelihood	Risk Rating	Risk Owner
			native/threatened species population declines within KNP	spread beyond the project area	vegetation - Long term maintenance requirements								
12	Transport of materials, equipment and personnel	Biodiversity	Frequent Injury/mortality of protected fauna	Driving vehicles on access roads during times of high fauna activity. Excessive speed on access roads. Inattention of drivers on potential for fauna impacts.	 Trigger EPBC Act thresholds for impacts on Commonwealth listed species, including Booroolong Frog and Smoky Mouse Potential regulatory action from agencies Financial penalties Reputational impacts Personal injury due to collision with large fauna including kangaroos, feral pigs, horses and deer 	4 - Major	3 - Possible	12 - High	- Biodiversity Management Plan - Transport Management Plan - Drivers Code of Conduct	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
13	Transport of materials, equipment and personnel	Biodiversity	Introduction and spread of weeds, pests and pathogens causing native/threatened species population declines within KNP	Vehicular movements from disturbed and contaminated areas beyond KNP into undisturbed areas within the project area and surrounding national park	 Impact to biodiversity in exceedance of the approved Project Spread of weeds in the National Park Smothering / impacts to native vegetation Long term maintenance requirements 	4 - Major	3 - Possible	12 - High	 Biodiversity Management Plan Weed, Pest and Pathogen Management Plan Weed and seed washdown inspections Washdown facility for plant Hygiene inspections of vehicles 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
14	Vegetation Clearing	Surface water	- Erosion and sedimentation - Contamination of surface water and breach of EPL water quality performance standards	Newly exposed sediment and top soil carried into catchments and watercourses during rainfall events	 Water pollution Loss of topsoil Impacts to aquatic habitat and fauna Potential regulatory action from agencies Financial penalties Reputational impacts 	4 - Major	3 - Possible	12 - High	 Water Management Plan Surface Water Management Plan Surface Water Monitoring Program Erosion and sediment control measures Clean water diversions Sediment basins and water treatment Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
15	Earthworks/ Roadworks	Surface water	 Contamination of surface water Breach of EPL water quality performance standards Dispersion of contaminants 	Exposed sediment carried into catchments and watercourses during rainfall events	 Water pollution Loss of topsoil Impacts to aquatic habitat and fauna Potential regulatory action from agencies Financial penalties Reputational impacts 	4 - Major	3 - Possible	12 - High	 Water Management Plan Surface Water Management Plan Baseline water quality data Surface Water Monitoring Program Erosion and sediment control measures Clean water diversions Process and intercepted water management Sediment basins and water treatment Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
16	Spoil emplacement	Surface Water	Contamination of surface water, breach of EPL water quality performance standards	Runoff from spoil stockpiles causes contaminated/polluted stormwater discharge into watercourses due to lack of controls or inadequately installed controls	- Adverse water quality impacts - Loss of amenity - Potential regulatory action from agencies	4 - Major	3 - Possible	12 - High	 Spoil Management Plan Water Management Plan Surface Water Management Plan Erosion and sediment control measures Clean water diversions Sediment basins and water treatment Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
17	Construction of waterway crossings and barge access infrastructure	Surface water	 Contamination of surface water breach of EPL water quality performance standards Dispersion of contaminants 	Construction activities in Yarrangobilly Creek and Wallace Creek without controls that prevent siltation and turbidity discharge being carried downstream	 Water pollution Impacts to aquatic habitat and fauna Potential regulatory action from agencies Financial penalties Reputational impacts 	4 - Major	3 - Possible	12 - High	 Water Management Plan Surface Water Management Plan Specific management measures implemented for working within creeks, rivers and riparian areas Surface Water Monitoring Program Erosion and sediment control measures Clean water diversions Process and intercepted water management Sediment basins and water treatment Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
18	Dredging activities	Surface water	Contamination of surface water, breach of EPL water quality performance standards	Disturbance of reservoir bed results in increased turbidity, siltation and dissolved oxygen levels	 Water pollution Impacts to aquatic habitat and fauna Potential regulatory action from agencies Financial penalties Reputational impacts 	4 - Major	3 - Possible	12 - High	 Water Management Plan Dredging Management Plan (for Exploratory Works if dredging) Surface Water Management Plan Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
19	Transport of materials, equipment and personnel	Surface water	Contamination of surface water, breach of EPL water quality performance standards	Vehicular spills along access road or within Project compounds	 Hydrocarbon pollution Potential regulatory action from agencies Financial penalties Reputational impacts 	3 - Moderate	3 - Possible	9 - Medium	 Water Management Plan Surface Water Management Plan Spill Response Procedure Training of drivers and relevant personnel Trigger Action Response Plan Refuelling and washdown in designated areas 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation





		Environmental	Dist					Initial	Piet T			Residual	Risk
	Activity	Aspect	Risk	Cause	Possible Outcome	Consequence	Likelihood	Risk Rating	Risk Treatment(s)	Consequence	Likelihood	Risk Rating	Owner
	Storage of hazardous materials	Surface water	Contamination of surface water, breach of EPL water quality performance standards	Spill of stored hazardous material escaping containment into waterways	 Hydrocarbon pollution Potential regulatory action from agencies Financial penalties Reputational impacts 	4 - Major	3 - Possible	12 - High	 Water Management Plan Surface Water Management Plan Bunded areas for storage of fuels and oils Spill Response Procedure Provision of spill response kits Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generatio
	Storage of hazardous materials	Groundwater	Contamination of groundwater	Spill or leaks of stored hazardous material dispersing into ground water	 Potential for irreparable damage to groundwater quality Impact to groundwater dependent species or ecosystems Damage to Karst features 	4 - Major	3 - Possible	12 - High	 Water Management Plan Groundwater Management Plan Groundwater Monitoring Program Bunded areas for storage of fuels and oils Spill Response Procedure Provision of spill response kits Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generati
	Tunnel construction	Groundwater	Contamination of groundwater, ground water level depletion	Interception of groundwater during tunnelling activities provides interface for contamination of groundwater and/or reduction in groundwater levels	 Impact to groundwater levels beyond those assessed Ecological impacts in dependent waterways and groundwater dependent ecosystems including karst features 	3 - Moderate	2 - Unlikely	6 - Medium	- Water Management plan - Groundwater Management Plan - Groundwater level and quality monitoring - Groundwater Dependent Ecosystem monitoring	3 - Moderate	1 - Rare	3 - Low	Future Generatio
	Tunnelling and spoil emplacement	Contamination	Contamination of soils by NOA and acid- forming materials, spread of contamination across the site an surrounds, potential for significant health hazards caused by naturally occurring asbestos	Irresponsible management and movement of contaminated spoil	 Potential for significant health hazards Long term contamination Potential regulatory action from agencies Financial penalties Reputational impacts 	5 - Severe	4 - Likely	20 - Extreme	- Spoil Management Plan - Training for all contractors - Geotechnical investigations to aid in predicting NOA presence	5 - Severe	2 - Unlikely	10 - Medium	Future Generatic
5	Earthworks/ Roadworks	Landform	Loss and/or degradation of topsoils and subsoils	Exposed sediment carried into catchments and watercourses during rainfall events due to lack of controls or inadequately installed controls	- Adverse water quality impacts - Loss of amenity - Potential regulatory action from agencies	4 - Major	3 - Possible	12 - High	 Water Management Plan Surface Water Management Plan Baseline water quality data Surface Water Monitoring Program Erosion and sediment control measures Clean water diversions Process and intercepted water management Sediment basins and water treatment Trigger Action Response Plan 	4 - Major	2 - Unlikely	8 - Medium	Future Generatic
6	Clearing and earthworks	Landform	Loss of visual amenity	Earthworks, spoil emplacement and vegetation clearing not adequately remediated following completion of the project.	- Amenity impacts to KNP - Loss of amenity for KNP users - Impacts inconsistent with project approval Reputational impacts	3 - Moderate	3 - Possible	9 - Medium	 Minimise soil and vegetation clearance Sensitive area plans / GIS mapping Rehabilitation Management Plan 	3 - Moderate	2 - Unlikely	3 - Low	Future Generatio
7	Clearing and earthworks	Landform	Loss of geodiversity features, fossils, boulder screes beyond those assessed in the project approval	Clearing outside the project footprint, plant operation and excavation outside project footprint	 Unapproved impacts beyond construction envelope Loss of geodiversity values Potential regulatory action from agencies Reputational impacts 	3 - Moderate	3 - Possible	9 - Medium	 Sensitive area plans / GIS mapping Heritage Management Plan identifies areas of conservation significance Unexpected finds protocol 	3 - Moderate	2 - Unlikely	3 - Low	Future Generatio
3	Spoil emplacement	Landform	Changes to landform and natural water flows	Earthworks, stockpiles, spoil emplacement and structures disrupting existing surface and groundwater regimes	 Groundwater level reduced Surface water flows in waterways cease to flow Unpredictable water quality impacts from changed water regime 	3 - Moderate	2 - Unlikely	6 - Medium	- Spoil Management Plans - Detailed plans for emplacement areas - Water Management Plan - Surface Water Management Plan	3 - Moderate	1 - Rare	3 - Low	Future Generatio
9	Earthworks, vegetation clearing, blasting, transport of plant	Heritage	Damage to heritage items, including culturally significant sites, artefacts and heritage values	Clearing outside the project footprint, plant operation and excavation outside project footprint, relocation of blasting not assessed for sensitive area/item impacts	 Unapproved impacts beyond project boundary Potential regulatory action from agencies Financial penalties Reputational impacts 	3 - Moderate	3 - Possible	9 - Medium	 Sensitive area plans / GIS mapping Heritage Management Plan identifies areas of conservation significance archival recording and / or salvage of items carried out as required by the Approval 	3 - Moderate	2 - Unlikely	3 - Low	Future Generation





N	A additution	Environmental	Risk	Course	Dessible Outsome	Comment	Likelihood	Initial		Com	Likelihood	Residual	Risk
NO	Activity	Aspect	RISK	Cause	Possible Outcome	Consequence	Likelihood	Risk Rating	Risk Treatment(s)	Consequence	Likelihood	Risk Rating	Owner
30	Actions of site personnel or members of public	Heritage	Theft of heritage items	Persons entering restricted areas unmonitored and using heritage documentation to locate items of interest	 Loss of items of cultural significance Impacts to relationships with traditional owners Potential regulatory impacts from agencies Reputational impacts 	2 - Minor	3 - Possible	6 - Medium	- Heritage Management Plan - Archival recording and salvage - Exclusion zones and defined clearing limits	2 - Minor	1 - Rare	2 - Low	Future Generation
31	Earthworks, vegetation clearing, blasting, transport of plant	Noise and vibration	Increased noise and vibration levels at sensitive receivers, particularly at Rock Forest	Noise levels from construction activates and transport of materials, equipment and personnel exceeds the levels assessed in the approval. Works change from those assessed. The project site is remote from sensitive receivers, noise impacts are more likely an issue at Rock Forest.	 Sleep disturbance at sensitive receiver locations Decreased amenity for KNP users in the locality Loss of support from local community 	3 - Moderate	3 - Possible	9 - Medium	- Construction Noise Management Plan - Traffic Management Plan	3 - Moderate	1 - Rare	3 - Low	Future Generation
32	Earthworks, blasting, transport of plant	Noise and vibration	Vibratory impacts to heritage items, geodiversity and structures	Vibrations from plant operation, transport, and blasting impacts exceed those assessed and cause structural damage to sensitive items	 Loss of items of cultural significance Impacts to relationships with traditional owners Potential regulatory impacts from agencies 	2 - Minor	2 - Unlikely	4 - Low	- Heritage Management Plan - Archival recording and salvage - Exclusion zones and defined clearing limits	2 - Minor	1 - Rare	2 - Low	Future Generation
34	Rock crushing/ screening	Noise and vibration	Increased noise and vibration levels at sensitive receivers	Rock crushing and screening activities situated too close to sensitive receivers	 Sleep disturbance at sensitive receiver locations Decreased amenity for KNP users in the locality Loss of support from local community 	3 - Moderate	3 - Possible	9 - Medium	 Construction Noise Management Plan Noise monitoring to evaluate impacts and establish additional mitigation where required 	3 - Moderate	1 - Rare	3 - Low	Future Generation
35	Rock crushing/ screening	Air Quality	Increased dust emissions	Rock crushing and screening activities not implementing adequate dust suppression mitigation	 Excessive dust emission/deposition in surrounding environment Air quality impacts exceed the approved project levels Adverse biodiversity impacts 	3 - Moderate	4 - Likely	12 - High	 Dust suppression through use of water cart Progressive stabilisation of the site 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
36	Earthworks, blasting, transport of plant	Air Quality	Visible dust plumes and deposition of dust on surfaces	Blasting and plant movements cause dust particle to become airborne and carried in wind to other areas	 Excessive dust emission/deposition in surrounding environment Air quality impacts exceed the approved project levels Adverse biodiversity impacts 	3 - Moderate	4 - Likely	12 - High	 Dust suppression through use of water cart Progressive stabilisation of the site 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
37	Vegetation clearing, spoil emplacement	Air Quality	Visible dust plumes and deposition of dust on surfaces, impacts to amenity, Dust generation from exposing of top soil and sub soil through vegetation removal,	Exposed sediment and stockpiled fines become airborne in strong winds and carried to other areas	 Excessive dust emission/deposition in surrounding environment Air quality impacts exceed the approved project levels Adverse biodiversity impacts 	3 - Moderate	4 - Likely	12 - High	 Dust suppression through use of water cart Spoil Management Plan Rehabilitation/stabilisation of cleared areas where possible 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
38	Spoil management, tunnelling	Air Quality / Waste	Release of airborne fibres from disturbed Naturally Occurring Asbestos (NOA)	Excavated materials containing NOA are not appropriately identified and/or contained following excavation from tunnel	 Airborne contamination and deposition to surrounding areas Potential for significant health hazards Long term contamination Potential regulatory action from agencies Financial penalties Reputational impacts 	5 - Severe	4 - Likely	20 - Extreme	- Spoil Management Plan - Geotechnical investigations to aid in predicting NOA presence	5 - Severe	2 - Unlikely	10 - Medium	Future Generation
39	Earthworks, roadworks	Waste	Excess use of natural resources and energy, production of greenhouse gases	Unnecessary operation/ idling of machinery and plant	 Excessive consumption of diesel and other resources Unnecessary production of greenhouse gases 	1 - Negligible	4 - Likely	4 - Low	- Training/instruction to machinery and plant operators to shut down equipment when not required	1 - Negligible	3 - Possible	3 - Low	Future Generation





		Environmentel						Initial				Residual	Risk
No	Activity	Environmental Aspect	Risk	Cause	Possible Outcome	Consequence	Likelihood	Risk Rating	Risk Treatment(s)	Consequence	Likelihood	Risk Rating	Owner
40	Storage / disposal of hazardous materials	Waste	Contamination of soil and water, unlawful disposal of waste	Inadequate storage of hazardous materials, inadequate spill management practices, improper disposal practices	 Contamination of soil and water in sensitive environment Potential regulatory action from agencies Financial penalties Loss of community support Reputational impacts 	4 - Major	3 - Possible	12 - High	 Surface Water Management Plan to address spills Spill Management Procedure Use of licensed disposal contractors for waste disposal which requires licensing Appropriate bunded storage of hazardous materials 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
41	Operation of accommodation camp	Waste	Excess use of natural resources and energy	Inefficient use of resources within the accommodation camp	- Excessive use of water and electricity	2 - Minor	4 - Likely	8 - Medium	 Energy efficient design of site facilities Water saving devices installed in camp facilities where possible 	2 - Minor	2 - Unlikely	4 - Low	Future Generation
42	Operation of accommodation camp	Waste	Odour impacts, contamination of soil and water in sensitive environment, excess waste sent to landfill	Inadequate management of camp waste including sewerage and mixed waste	 Unlawful disposal of waste Excess waste generation Contamination of waste streams Contamination of soil and water Potential regulatory action from agencies 	4 - Major	3 - Possible	12 - High	 Waste facilities available at the camps Use of licensed waste disposal contractors Waste tracking Regular inspection of controls 	4 - Major	2 - Unlikely	8 - Medium	Future Generation
43	Transport of materials, equipment and personnel	Waste	Unnecessary production of Greenhouse gases	Materials shipped from distant locations, excessive personal vehicle usage, repeated movements back and forth from site	- Unnecessary production of greenhouse gases - Impacts of the project exceed those assessed in the EIS	2 - Minor	5 - Almost Certain	10 - Medium	 Transport Management Plan implemented Procurement of local materials to minimise shipping distances where possible Communal transport to site for personnel (including buses and prohibition of personal vehicle use) where possible Personnel to remain on site to reduce commute time and transport requirements 	2 - Minor	2 - Unlikely	4 - Low	Future Generation
44	Vegetation Clearing	Waste	Excessive production of Greenhouse gases	Excessive clearing of vegetation resulting in increased greenhouse gas emission from released carbon storage in decomposing vegetation	- Unnecessary production of greenhouse gases - Impacts of the project exceed those assessed in the EIS	2 - Minor	3 - Possible	6 - Medium	- Exclusion fencing to identify areas not to be cleared	2 - Minor	1 - Rare	2 - Low	Future Generation
45	Hot works and plant operations	Emergency	Ignition of bushfire	Sparks from machinery or hot work activities ignites combustible vegetation and fire gets out of control	 Significant impact to KNP through bushfire Potential destruction of project infrastructure and equipment Potential for fatality/injury to personnel and members of the public Damage to public property and adjacent properties Loss of biodiversity Project delays Significant reputational impact Potential regulatory actions from agencies Financial penalties 	5 - Severe	4 - Likely	20 - Extreme	 Natural Hazard Management Plan Continuous monitoring of fire hazard throughout bushfire season Suspension of fire risk work on days of elevated fire danger in accordance with the EMP Fire preparedness mitigation measures implemented on fire danger days Relevant personnel trained in rapid response to extinguish potential ignitions to prevent bushfire escalation Provision of firefighting equipment throughout the project site 	5 - Severe	3 - Possible	15 - High	Future Generation
46	Working in bushfire prone areas	Emergency	Damage to construction site and works by bushfire	Siting of infrastructure and personnel in bushfire prone areas without appropriate bushfire mitigation in place.	 Damage to construction site and works Project delays Safety impacts 	3 - Moderate	4 - Likely	12 - High	 Pre position fire fighting equipment Safety and emergency systems and procedures Implement preparatory actions of Natural Hazard Management Plan 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
47	Earthworks	Emergency	Localised flooding within construction envelope	Alterations to existing hydrological regime through earthworks, blasting, basin construction, tunnelling and building construction beyond those assessed	 Localised flooding Damage to project infrastructure Project access/egress interrupted Water quality impacts 	3 - Moderate	2 - Unlikely	6 - Medium	 Consideration of hydrology throughout detailed design Location of stockpiles and structures above flood zones where possible 	3 - Moderate	1 - Rare	3 - Low	Future Generation
48	Earthworks/ Roadworks	Traffic	Disturbance / traffic delays to local residents	Roadworks on local roads blocking or excessively delaying traffic movements and thoroughfare.	 Traffic delays on local and regional roads Increased safety hazard Adverse reputational impacts Increased noise and air quality impacts 	3 - Moderate	4 - Likely	12 - High	- Transport Management Plan - Engagement with community to manage expectations	3 - Moderate	3 - Possible	9 - Medium	Future Generation





No	Activity	Environmental Aspect	Risk	Cause	Possible Outcome	Consequence	Likelihood	Initial Risk Rating	Risk Treatment(s)	Consequence	Likelihood	Residual Risk Rating	Risk Owner
49	Transport of materials, equipment and personnel	Traffic	Increased traffic volumes and congestion, increased road noise, degradation of roadways, traffic delays	Heavy and light vehicles moving in convoys through local towns to the project site.	 Traffic delays on local and regional roads Increased safety hazard Adverse reputational impacts Increased noise and air quality impacts 	3 - Moderate	4 - Likely	12 - High	 Transport Management Plan Manage timing of OSOM movements Driver code of conduct Engagement with community 	3 - Moderate	3 - Possible	9 - Medium	Future Generation
50	Construction activities	Socio economic and KNP	Loss of public facilities and KNP recreational facilities, loss of access of areas to KNP for public use.	Construction activities inhibiting public access to KNP and reservoir facilities including camping areas and boat ramps to reservoirs	- Loss of community support for the project	3 - Moderate	3 - Possible	9 - Medium	 Clearly signposted signage indicated area closures and timeframes Minimisation of project traffic movements during peak recreational periods 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation
51	Inflow of workforce to local area	Socio economic and KNP	Business impacts, increased housing demand	Workforce size relocating to local area	Housing rental/purchase prices increase due to increased demand - Local services struggle to meet demands - Loss of community support for the project	2 - Minor	3 - Possible	6 - Medium	 Establishment of Pacific Hills development to provide accommodation for workforce Encourage personnel to purchase local produce and use local business to stimulate positive economic growth in the locality 	2 - Minor	2 - Unlikely	4 - Low	Future Generation
52	Working in bushfire prone areas	Emergency	Damage to construction site and works by bushfire	Siting of infrastructure and personnel in bushfire prone areas without appropriate bushfire mitigation in place.	- Damage to construction site and works - Project delays - Safety impacts	3 - Moderate	4 - Likely	12 - High	 Pre position fire fighting equipment Safety and emergency systems and procedures Implement preparatory actions of Natural Hazard Management Plan 	3 - Moderate	2 - Unlikely	6 - Medium	Future Generation







APPENDIX C - EXAMPLE INVENTORY OF POLLUTANTS

Updated pollutant register to be found at: include server reference

Location	Phase	Classification	Class	Sub	PG	Typical (L) (kg for explosives only)	Typical quantity (tonnes)	Storage type/ arrangement	Comments
Main camp (Lobs Hole)	Construction	Corrosive	8	-	111	2,000	2 Wastewater Treatment Plant		
Main camp (Lobs	Construction	Explosives	1.1	D	-	10,000	10	Magazine Store	
Hole)		Flammable gases	2	2.1	-	15,200	9.12	Warehouse	Made up of aerosols, sprays and cleaning agents
		Flammable	3	-	П	100	0.08	Warehouse	
		liquid			111	28,500	22.8	Warehouse	Stored more at least 20 m from site boundary (APZ)
		Corrosive	8	-	П	300	0.3	Warehouse	
MAT portal	Construction	Explosives	1.1	D	-	10,000	10	Ventilated Magazine Store	
		Corrosive	8	-	Ш	5,000	5	Process Water Treatment Plant	
Talbingo adit construction compound	Construction	Corrosive	8	-	Ш	22,500	225	Process Water Treatment Plant	
ECVT Portal	Construction	Explosives	1.1	D	-	10,000	10	Ventilated Magazine Store	
		Corrosive	8	-	 	16,000	16	Process Water Treatment Plant	
Marica accommodation camp	Construction	Corrosive	8	-	 	1,150	1.15	Wastewater Treatment Plant	
Headrace surge shaft	Construction	Corrosive	8	-	 	16,000	16	Process Water Treatment Plant	
Tantangara construction	Construction	Explosives	1.1	D	-	10,000	10	Ventilated Magazine Store	
compound		Corrosive	8	-	 	22,500	22.5	Process Water Treatment Plant	






Location	Phase	Classification	Class	Sub	PG	Typical (L) (kg for explosives only)	Typical quantity (tonnes)	Storage type/ arrangement	Comments
Tantangara accommodation camp	Construction	Corrosive	8	-	 	850	0.85	Wastewater Treatment Plant	
Rock Forest logistics laydown	Construction	Combustible liquid	-	-	-	320,000	-	-	Combustible liquid not stored with flammable liquids and so does not have a SEPP 33 screening threshold.






APPENDIX E - EPL PREMISE AREA MAPS

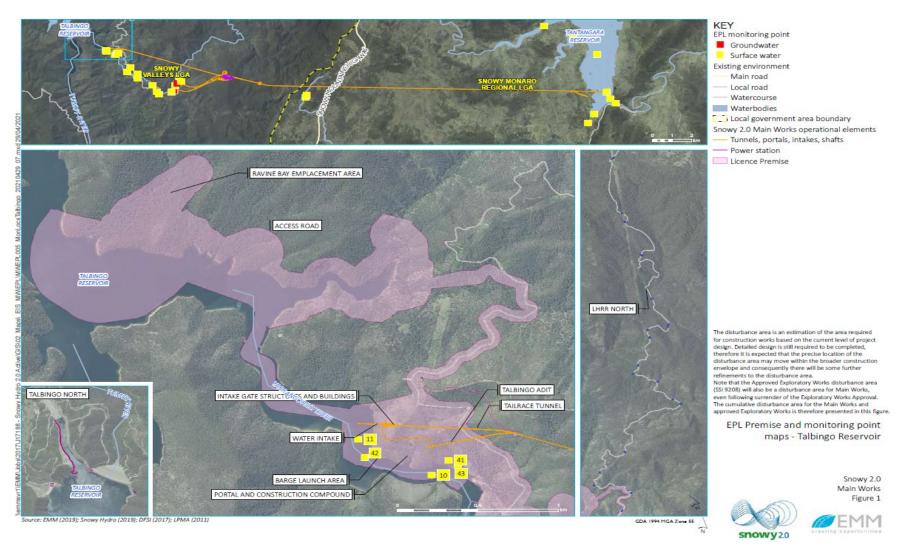






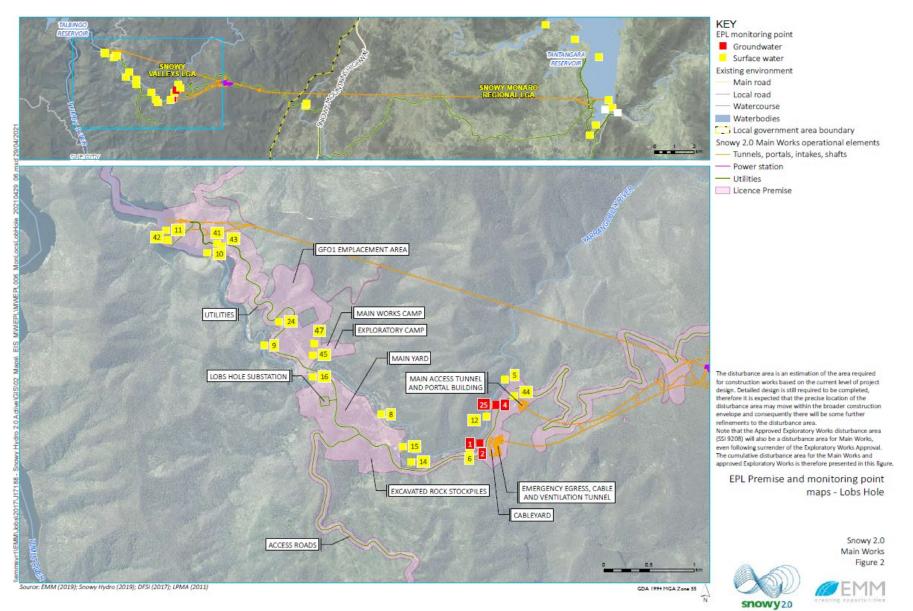






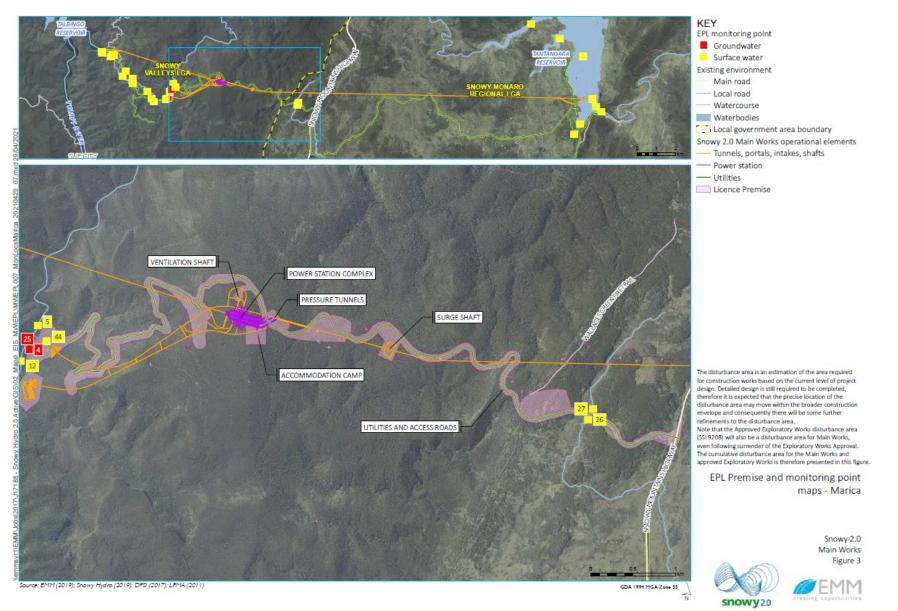






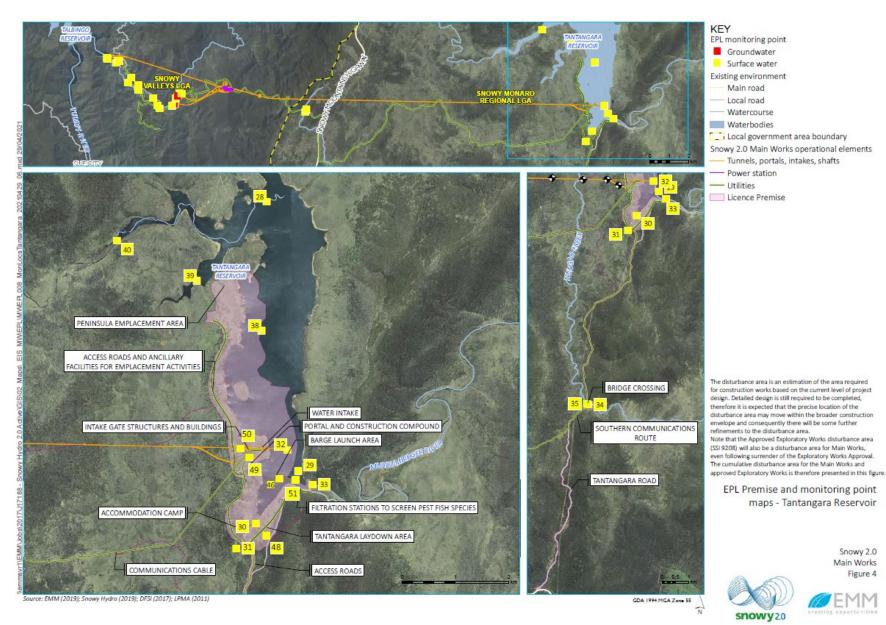

S2-FGJV-ENV-PLN-0091-Main Works Pollution Incident Response Management Plan | Page 61 of 62





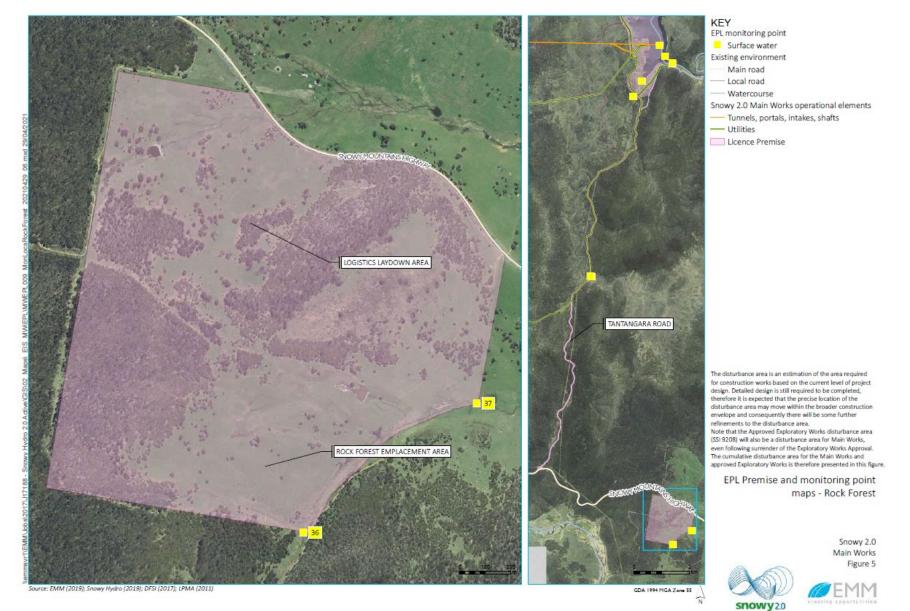

S2-FGJV-ENV-PLN-0091-Main Works Pollution Incident Response Management Plan | Page 62 of 62
